

ID	Task Name	Duration	Start	Finish	Predecessors	2010																
						1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		3rd Quarter				
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
1	AKV292 Seldovia Harbor Improvements	526 days	Mon 6/15/09	Mon 6/20/11																		
48	RA-538 Design and Construction	671 days	Tue 11/9/10	Tue 6/4/13																		
49	Project Acceptance & Funding	21 days	Tue 11/9/10	Tue 12/7/10																		
53	Project Start	41 days	Tue 4/26/11	Tue 6/21/11																		
56	Project Management Plan Update	59 days	Wed 6/22/11	Mon 9/12/11																		
57	PDT Provides new Budget for Design & D	21 days	Wed 6/22/11	Wed 7/20/11	54																	
58	Customer Reivew of PMP	15 days	Thu 8/11/11	Wed 8/31/11	57FS+15 days																	
59	Finalize PMP	5 days	Thu 9/1/11	Wed 9/7/11	58																	
60	Signed PMP	3 days	Thu 9/8/11	Mon 9/12/11	59																	
61	Engineering & Design	108 days	Thu 6/23/11	Mon 11/21/11																		
62	Scope Design	30 days	Thu 6/23/11	Thu 10/20/11	54FS+60 days																	
63	Selection Criteria	5 days	Fri 10/21/11	Thu 10/27/11	62																	
64	Meeting with Customer on Design	1 day	Fri 10/28/11	Fri 10/28/11	63																	
65	Final RFP Package for PDT Review	5 days	Mon 10/31/11	Fri 11/4/11	64																	
66	DQR/ITR	5 days	Mon 11/7/11	Fri 11/11/11	65																	
67	Incorporate Comments	5 days	Mon 11/14/11	Fri 11/18/11	66																	
68	Final Design Complete	1 day	Mon 11/21/11	Mon 11/21/11	67																	
69	Environmental	80 days	Wed 6/22/11	Tue 10/11/11																		
70	Prepare documents	15 days	Wed 6/22/11	Tue 7/12/11	54																	
71	SHPO	25 days	Wed 7/13/11	Tue 8/16/11	70																	
72	F&W Coordination	25 days	Wed 7/13/11	Tue 8/16/11	70																	
73	Section 404(b)(1) Analysis	25 days	Wed 7/13/11	Tue 8/16/11	70																	
74	Record of Descision	25 days	Wed 7/13/11	Tue 8/16/11	70																	
75	Section 103 Evaluation	25 days	Wed 7/13/11	Tue 8/16/11	70																	
76	Statement of Findings	25 days	Wed 7/13/11	Tue 8/16/11	70																	
77	Coastal Consistency	45 days	Wed 7/13/11	Tue 9/13/11	70																	
78	Draft Final	10 days	Wed 8/17/11	Tue 8/30/11	74																	
79	Pre-NEPA Meeting with Customer	1 day	Wed 8/31/11	Wed 8/31/11	78																	
80	Public Review	25 days	Wed 8/31/11	Tue 10/4/11	78																	
81	Signed FONSI	5 days	Wed 10/5/11	Tue 10/11/11	80																	
82	Real Estate	80 days	Wed 6/22/11	Tue 10/11/11																		
83	Obtain Permits for Construction	80 days	Wed 6/22/11	Tue 10/11/11	54																	
84	Cost Estimate	25 days	Mon 11/7/11	Fri 12/9/11																		
85	Develop 100% CWE	15 days	Mon 11/7/11	Fri 11/25/11	65																	
86	IGE	10 days	Mon 11/28/11	Fri 12/9/11	85																	
87	BCOE Review	29 days	Tue 11/22/11	Fri 12/30/11																		
88	BCOE Package for Review	3 days	Tue 11/22/11	Thu 11/24/11	69,68,82																	
89	Review	10 days	Fri 11/25/11	Thu 12/8/11	88																	
90	Incorporate Comments	5 days	Fri 12/9/11	Thu 12/15/11	89																	
91	Backcheck	3 days	Fri 12/16/11	Tue 12/20/11	90																	
92	Certification	3 days	Wed 12/21/11	Fri 12/23/11	91																	
93	Package for RFP	5 days	Mon 12/26/11	Fri 12/30/11	92																	
94	Contracting - Design-Build	169 days	Wed 7/20/11	Mon 3/12/12																		
95	Source Sought	20 days	Wed 7/20/11	Thu 10/27/11	62																	
96	Prepare Front End	15 days	Fri 10/21/11	Thu 11/10/11	62																	
97	Prepare for Legal Review	10 days	Fri 11/11/11	Thu 11/24/11	96																	
98	Request for Proposals	25 days	Mon 1/2/12	Fri 2/3/12	97,93																	
99	Solicitation Review	10 days	Mon 2/6/12	Fri 2/17/12	98																	
100	Award	5 days	Mon 2/20/12	Fri 2/24/12	99																	
101	Bonds	10 days	Mon 2/27/12	Fri 3/9/12	100																	

Project: AKV292 Seldovia Schedule ve
Date: Thu 9/1/11

Task  Milestone  External Tasks 
 Split  Summary  External Milestone 
 Progress  Project Summary  Deadline 


Page 1

ID	Task Name	Duration	Start	Finish	Predecessors	2010																
						arter		3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
						May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
102	Legal Review	3 days	Mon 2/27/12	Wed 2/29/12	100																	
103	Notice to Proceed	1 day	Mon 3/12/12	Mon 3/12/12	102,101																	
104	Construction	281 days	Tue 3/27/12	Tue 4/23/13																		
105	Pre-Design/Construction Meeting	1 day	Tue 3/27/12	Tue 3/27/12	103FS+10 days																	
106	Construct Project	260 days	Wed 3/28/12	Tue 3/26/13	105																	
107	Construction Complete	1 day	Wed 3/27/13	Wed 3/27/13	106																	
108	Final Inspection	1 day	Thu 3/28/13	Thu 3/28/13	107																	
109	Contract Closeout	15 days	Fri 3/29/13	Thu 4/18/13	108																	
110	Final Invoice	3 days	Fri 4/19/13	Tue 4/23/13	109																	
111	Project Closeout	33 days	Fri 4/19/13	Tue 6/4/13																		
112	Physical Closeout	10 days	Fri 4/19/13	Thu 5/2/13	109																	
113	Fiscal Closeout	30 days	Wed 4/24/13	Tue 6/4/13	110																	



Project: AKV292 Seldovia Schedule ve
Date: Thu 9/1/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

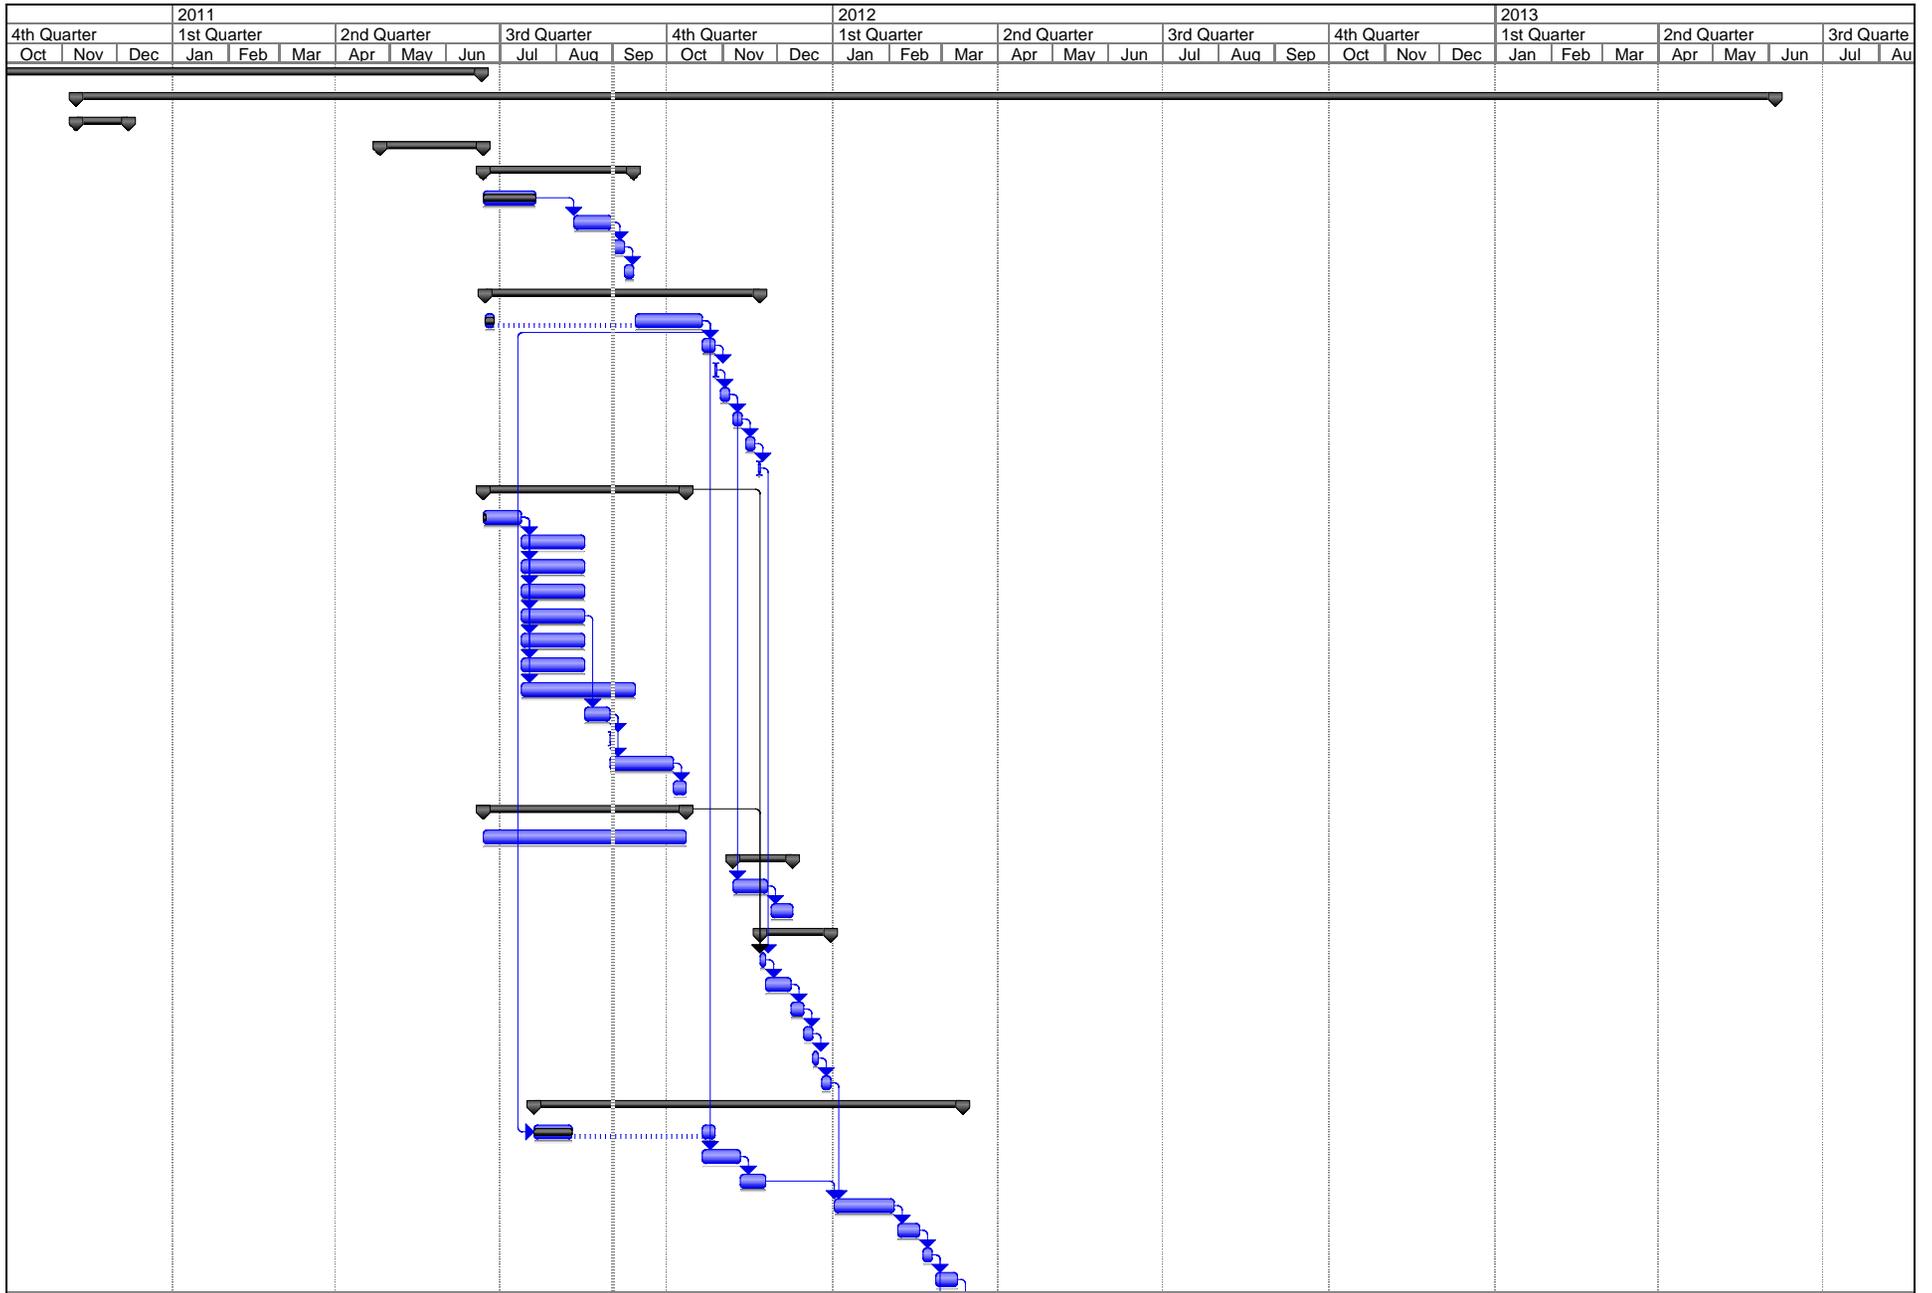

Project: AKV292 Seldovia Schedule ve
Date: Thu 9/1/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

