


ID	Task Name	Duration	Start	Finish	Predecessors	Timeline																	
						2nd Quarter				2nd Half			4th Quarter			1st Half			2nd Quarter			2nd Half	
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Bethel Small Boat Harbor	533 days	Thu 7/1/10	Mon 7/16/12		[Timeline bars for Bethel Small Boat Harbor]																	
2	Kickoff Meeting	1 day	Thu 7/1/10	Thu 7/1/10		[Timeline bar for Kickoff Meeting]																	
3	Develop PMP	529.82 days	Fri 7/2/10	Thu 7/12/12		[Timeline bars for Develop PMP]																	
11	Site Visit	1 day	Thu 9/9/10	Thu 9/9/10		[Timeline bar for Site Visit]																	
12	Trip Report	11 days	Fri 9/10/10	Fri 9/24/10	11	[Timeline bar for Trip Report]																	
13	Public Involvement	305 days	Wed 10/6/10	Tue 12/6/11	12	[Timeline bars for Public Involvement]																	
15	Engineering and Design	403 days	Thu 7/1/10	Tue 1/17/12		[Timeline bars for Engineering and Design]																	
26	Review (ITR)	6 days	Tue 1/10/12	Tue 1/17/12		[Timeline bar for Review (ITR)]																	
30	Environmental (EA)	200 days	Tue 6/21/11	Mon 3/26/12		[Timeline bar for Environmental (EA)]																	
41	Real Estate	532 days	Fri 7/2/10	Mon 7/16/12		[Timeline bars for Real Estate]																	
44	Cost Estimate	69 days	Thu 4/28/11	Tue 8/2/11		[Timeline bar for Cost Estimate]																	
46	Project Complete	28 days	Mon 3/12/12	Wed 4/18/12		[Timeline bar for Project Complete]																	
52	Bethel O&M - Launch Ramps Construction	538 days	Wed 2/15/12	Fri 3/7/14		[Timeline bars for Bethel O&M - Launch Ramps Construction]																	
53	Receive Denali Commission Funds	1 day	Tue 6/26/12	Tue 6/26/12		[Timeline bar for Receive Denali Commission Funds]																	
54	Signed MOA with Bethel	21 days	Fri 6/15/12	Fri 7/13/12		[Timeline bar for Signed MOA with Bethel]																	
55	Receive City of Bethel Funds	3 days	Mon 7/16/12	Wed 7/18/12	54	[Timeline bar for Receive City of Bethel Funds]																	
56	Received O&M Funds	9 days	Wed 2/15/12	Mon 2/27/12		[Timeline bar for Received O&M Funds]																	
57	Revise Plans & Specs	1 day	Mon 4/23/12	Tue 6/12/12		[Timeline bar for Revise Plans & Specs]																	
58	Bid Schedule	6 days	Mon 5/28/12	Mon 6/4/12	57	[Timeline bar for Bid Schedule]																	
59	NEPA Amendment - Signed by COL	10 days	Tue 3/13/12	Mon 3/26/12	56FS+10 days	[Timeline bar for NEPA Amendment - Signed by COL]																	
60	Real Estate Certification from City	30 days	Mon 6/4/12	Fri 7/13/12		[Timeline bar for Real Estate Certification from City]																	
61	IFB	167 days	Wed 2/22/12	Thu 10/11/12		[Timeline bars for IFB]																	
84	Construction Phase	291 days	Fri 12/7/12	Fri 1/17/14		[Timeline bars for Construction Phase]																	
85	Pre-Construction Meeting	1 day	Fri 12/7/12	Fri 12/7/12		[Timeline bar for Pre-Construction Meeting]																	
86	Construction	260 days	Mon 12/10/12	Fri 12/6/13	85	[Timeline bar for Construction]																	
87	Construction Complete	1 day	Mon 12/9/13	Mon 12/9/13	86	[Timeline bar for Construction Complete]																	
88	Inspection Report	14 days	Tue 12/10/13	Fri 12/27/13	87	[Timeline bar for Inspection Report]																	
89	Contract Closeout	14 days	Mon 12/30/13	Thu 1/16/14	88	[Timeline bar for Contract Closeout]																	
90	After Action Review	1 day	Fri 1/17/14	Fri 1/17/14	89	[Timeline bar for After Action Review]																	
91	Project Closeout	36 days	Fri 1/17/14	Fri 3/7/14		[Timeline bars for Project Closeout]																	
92	Physical Closeout	3 days	Fri 1/17/14	Tue 1/21/14	89	[Timeline bar for Physical Closeout]																	
93	Financial Closeout	30 days	Wed 1/22/14	Tue 3/4/14	92	[Timeline bar for Financial Closeout]																	
94	Closed Out	3 days	Wed 3/5/14	Fri 3/7/14	93	[Timeline bar for Closed Out]																	

Project: Eek Draft Schedule 0.45mpp
Date: Tue 1/7/14

Task: [Blue bar] Progress [Grey bar] Summary [Arrow bar] External Tasks [Grey bar] Deadline [Green arrow]

Split: [Dotted bar] Milestone [Diamond] Project Summary [Arrow bar] External Milestone [Diamond]

Page 1

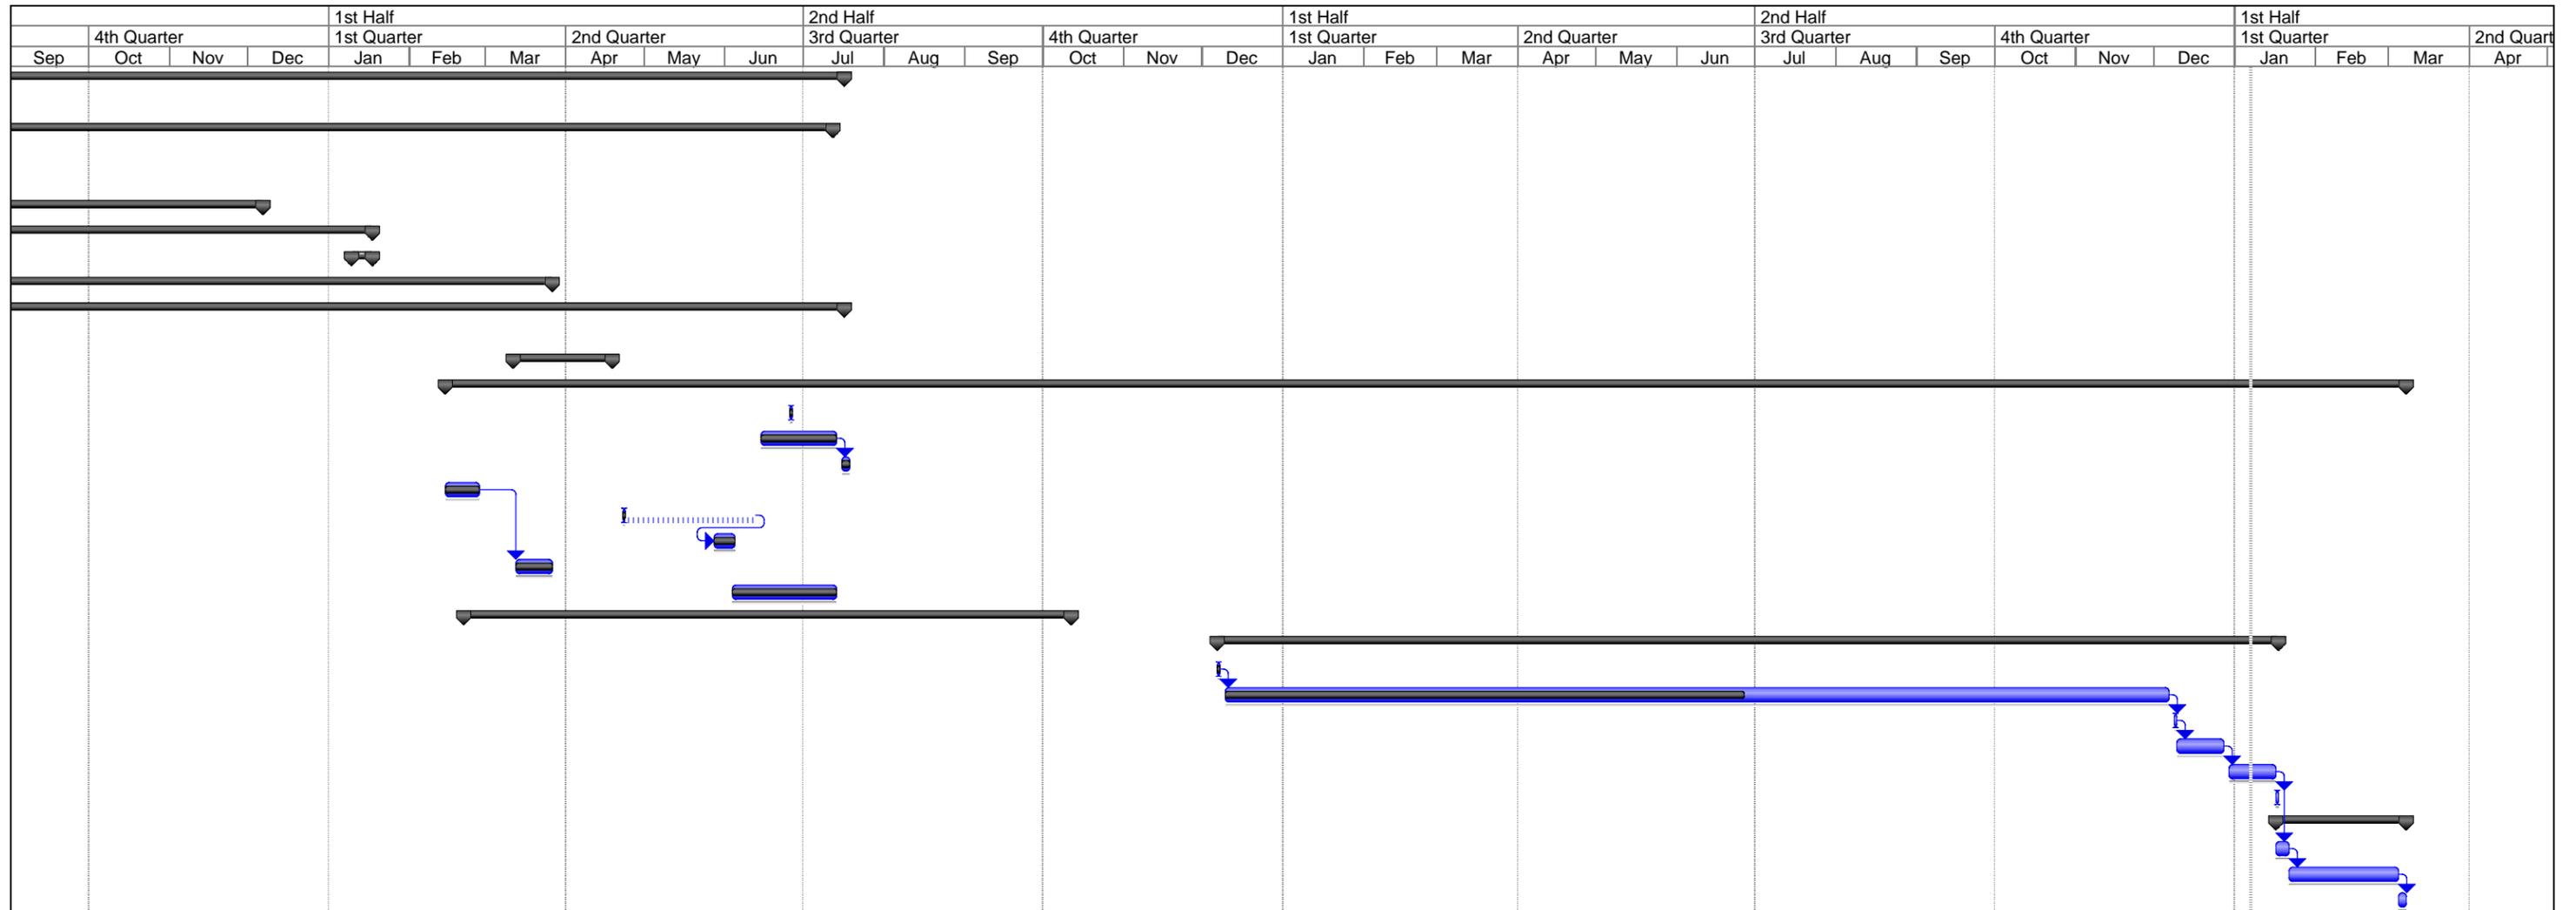

Project: Eek Draft Schedule 0.45mpp
Date: Tue 1/7/14

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
