


| ID | Task Name                              | Duration        | Start              | Finish             | Predecessors | 2010        |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
|----|--|-----------------|--------------------|--------------------|--------------|-------------|-----|-------------|-----|-------------|-----|-------------|-----|-----|-----|-----|-----|--|--|--|--|--|
|    |  |                 |                    |                    |              | 1st Quarter |     | 2nd Quarter |     | 3rd Quarter |     | 4th Quarter |     |     |     |     |     |  |  |  |  |  |
|    |  |                 |                    |                    |              | Jan         | Feb | Mar         | Apr | May         | Jun | Jul         | Aug | Sep | Oct | Nov | Dec |  |  |  |  |  |
| 1  | AKV292 Seldovia Harbor Improvements    | 526 days        | Mon 6/15/09        | Mon 6/20/11        |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 48 | RA-538 Design and Construction         | 860 days        | Tue 11/9/10        | Mon 2/24/14        |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 49 | Project Acceptance & Funding           | 21 days         | Tue 11/9/10        | Tue 12/7/10        |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 53 | Project Start                          | 41 days         | Tue 4/26/11        | Tue 6/21/11        |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 56 | Project Management Plan Update         | 209 days        | Wed 6/22/11        | Mon 4/9/12         |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 57 | PDT Provides new Budget for Design & C | 21 days         | Wed 6/22/11        | Wed 7/20/11        | 54           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 58 | Customer Reivew of PMP                 | 2 days          | Fri 3/2/12         | Mon 3/5/12         | 57FS+15 days |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 59 | Finalize PMP                           | 5 days          | Thu 3/29/12        | Wed 4/4/12         | 58           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 60 | Signed PMP                             | 3 days          | Thu 4/5/12         | Mon 4/9/12         | 59           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 61 | <b>Engineering &amp; Design</b>        | <b>279 days</b> | <b>Thu 6/23/11</b> | <b>Tue 7/17/12</b> |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 62 | Scope Design                           | 45 days         | Thu 6/23/11        | Thu 11/10/11       | 54FS+60 days |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 63 | Interim Design Package for Review      | 70 days         | Mon 2/27/12        | Fri 6/1/12         |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 64 | Meeting with Customer on Design        | 1 day           | Mon 6/11/12        | Mon 6/11/12        | 63FS+5 days  |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 65 | Final Design for PDT Review            | 10 days         | Tue 6/12/12        | Mon 6/25/12        | 64           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 66 | DQR/ITR                                | 10 days         | Tue 6/26/12        | Mon 7/9/12         | 65           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 67 | Incorporate Comments                   | 5 days          | Tue 7/10/12        | Mon 7/16/12        | 66           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 68 | Final Design Complete                  | 1 day           | Tue 7/17/12        | Tue 7/17/12        | 67           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 69 | <b>Environmental</b>                   | <b>266 days</b> | <b>Wed 6/22/11</b> | <b>Wed 6/27/12</b> |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 70 | Prepare documents                      | 80 days         | Wed 6/22/11        | Tue 10/11/11       | 54           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 71 | F&W Coordination                       | 85 days         | Wed 10/12/11       | Tue 2/7/12         | 70           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 72 | Section 404(b)(1) Analysis             | 25 days         | Wed 10/12/11       | Wed 4/4/12         | 70           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 73 | Record of Descision                    | 25 days         | Thu 3/29/12        | Wed 5/2/12         | 70           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 74 | Draft Final                            | 10 days         | Thu 5/3/12         | Wed 5/16/12        | 73           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 75 | Pre-NEPA Meeting with Customer         | 1 day           | Thu 5/17/12        | Thu 5/17/12        | 74           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 76 | Public Review                          | 25 days         | Thu 5/17/12        | Wed 6/20/12        | 74           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 77 | Signed ROD                             | 5 days          | Thu 6/21/12        | Wed 6/27/12        | 76           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 78 | <b>Real Estate</b>                     | <b>30 days</b>  | <b>Thu 3/29/12</b> | <b>Wed 5/9/12</b>  |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 79 | Obtain Permits for Construction        | 30 days         | Thu 3/29/12        | Wed 5/9/12         | 62           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 80 | <b>Cost Estimate</b>                   | <b>75 days</b>  | <b>Mon 6/4/12</b>  | <b>Fri 9/14/12</b> |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 81 | Develop 100% CWE                       | 10 days         | Mon 6/4/12         | Fri 6/15/12        | 63           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 82 | IGE                                    | 10 days         | Mon 9/3/12         | Fri 9/14/12        | 103          |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 83 | <b>BCOE Review</b>                     | <b>22 days</b>  | <b>Wed 7/18/12</b> | <b>Thu 8/16/12</b> |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 84 | BCOE Package for Review                | 1 day           | Wed 7/18/12        | Wed 7/18/12        | 69,68,78     |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 85 | Review                                 | 10 days         | Thu 7/19/12        | Wed 8/1/12         | 84           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 86 | Incorporate Comments                   | 5 days          | Thu 8/2/12         | Wed 8/8/12         | 85           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 87 | Backcheck                              | 3 days          | Thu 8/9/12         | Mon 8/13/12        | 86           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 88 | Certification                          | 3 days          | Tue 8/14/12        | Thu 8/16/12        | 87           |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 89 | <b>MOA with City for Funds</b>         | <b>90 days</b>  | <b>Mon 4/16/12</b> | <b>Fri 8/17/12</b> |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |
| 90 | Develop MOA                            | 30 days         | Mon 4/16/12        | Fri 5/25/12        |              |             |     |             |     |             |     |             |     |     |     |     |     |  |  |  |  |  |

Project: AKV292 Seldovia Schedule v1  
Date: Wed 3/28/12

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone



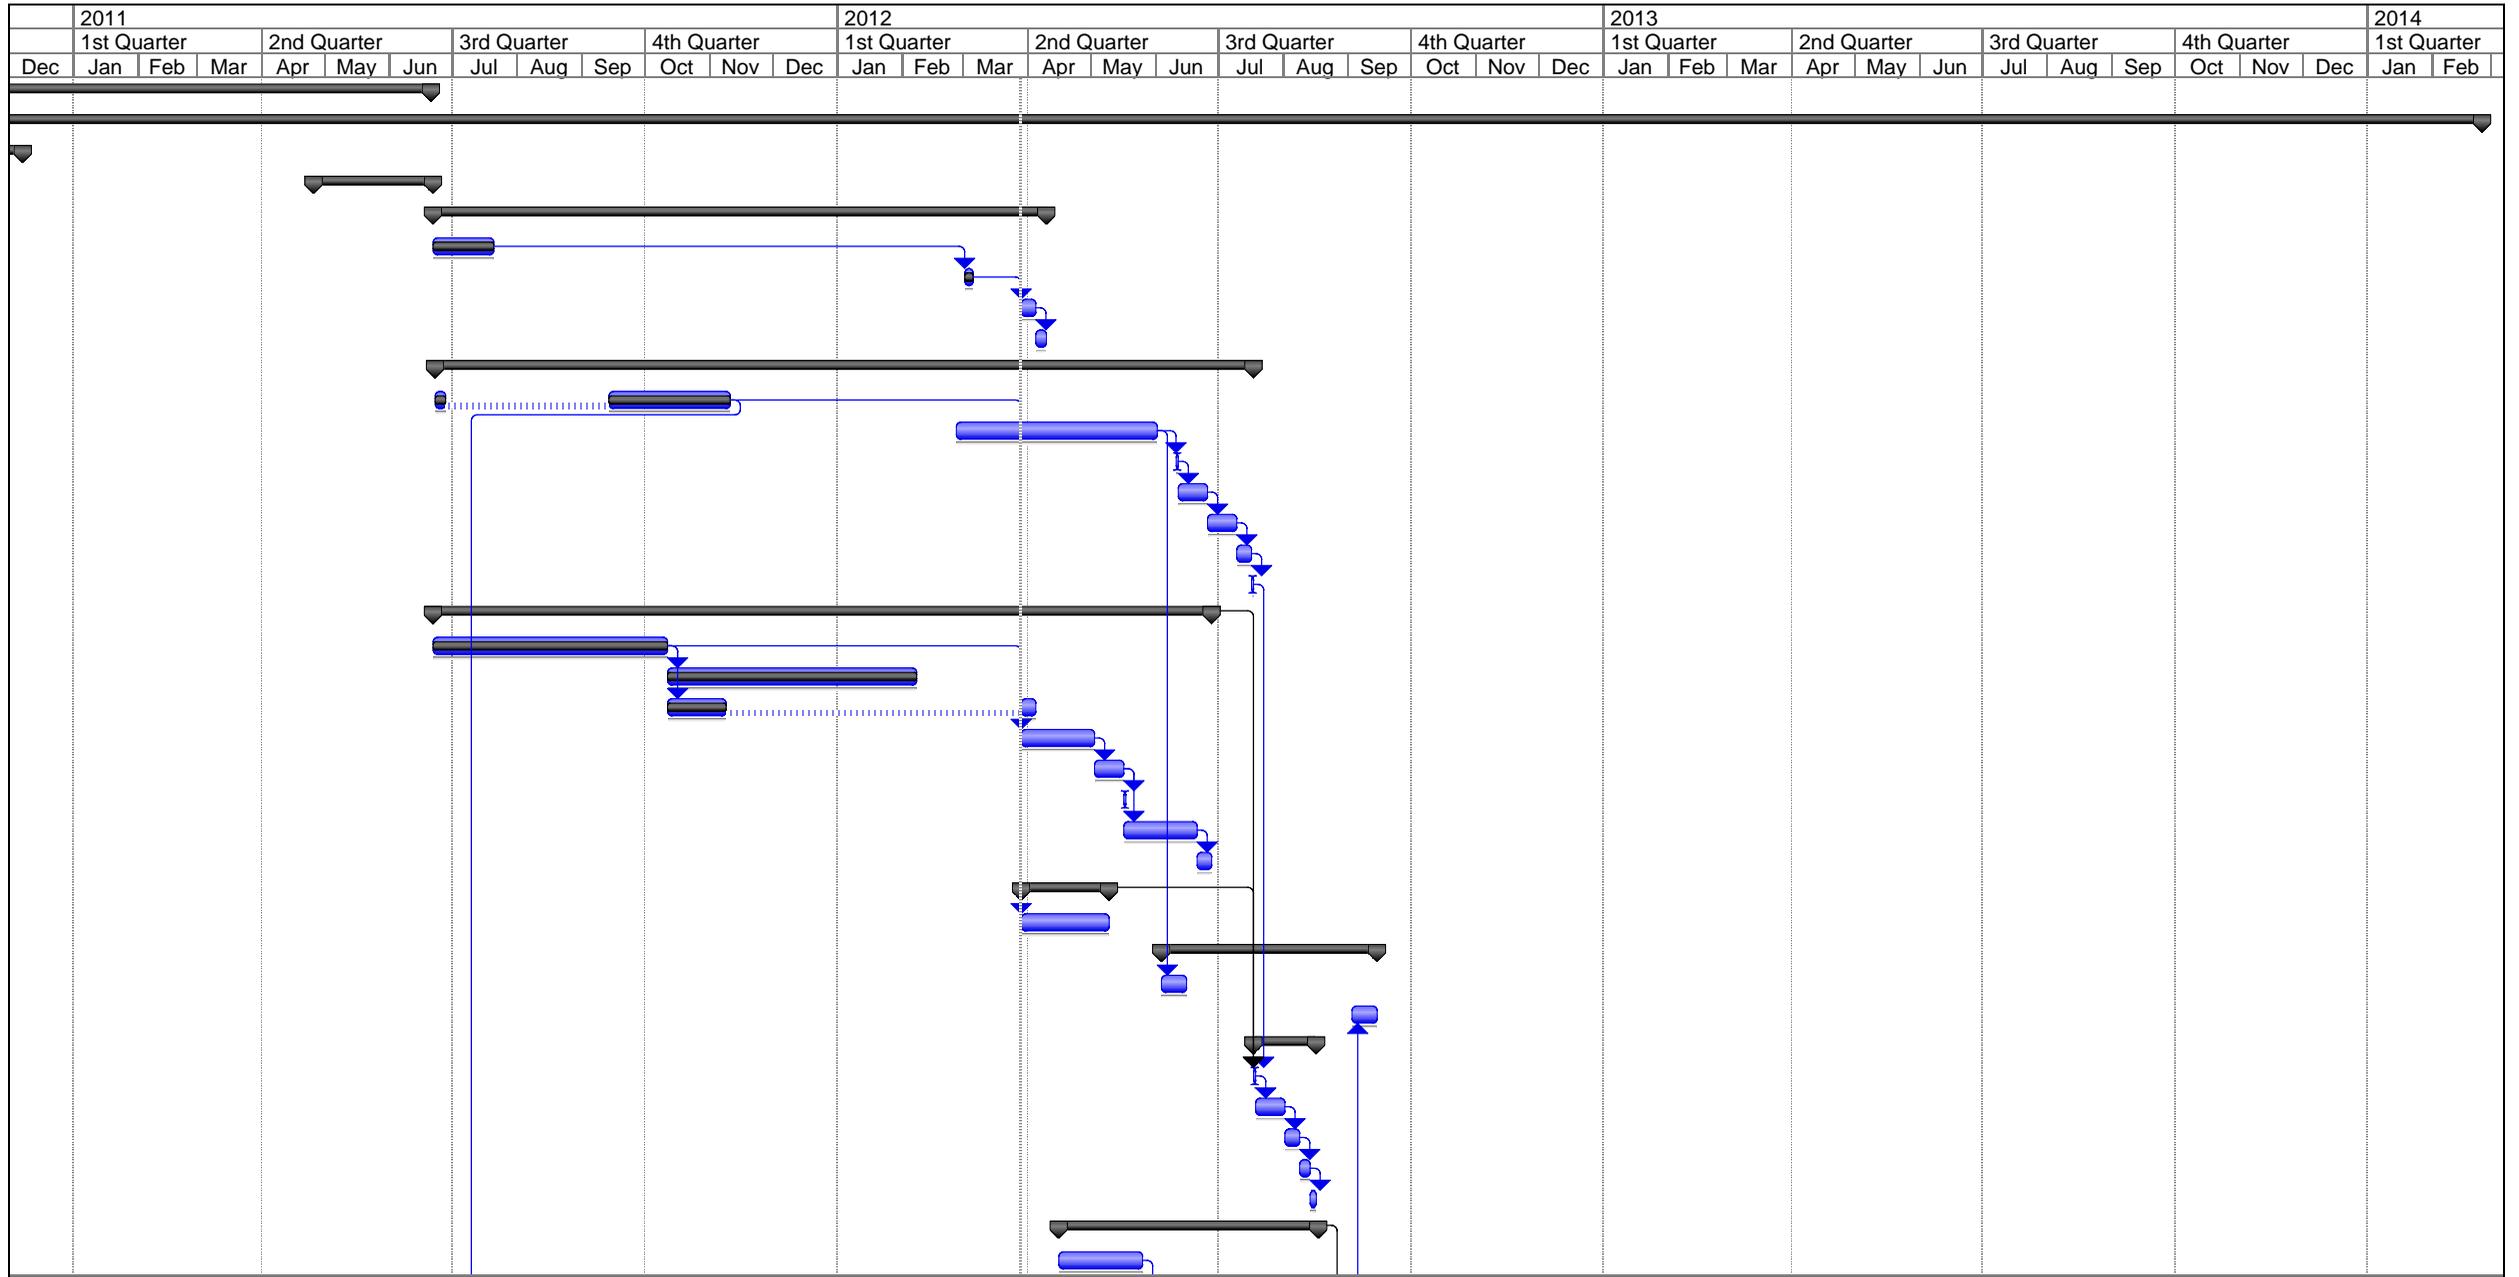

Project: AKV292 Seldovia Schedule v1  
 Date: Wed 3/28/12

Task  
 Split



Progress  
 Milestone



Summary  
 Project Summary




External Tasks  
 External Milestone



Deadline



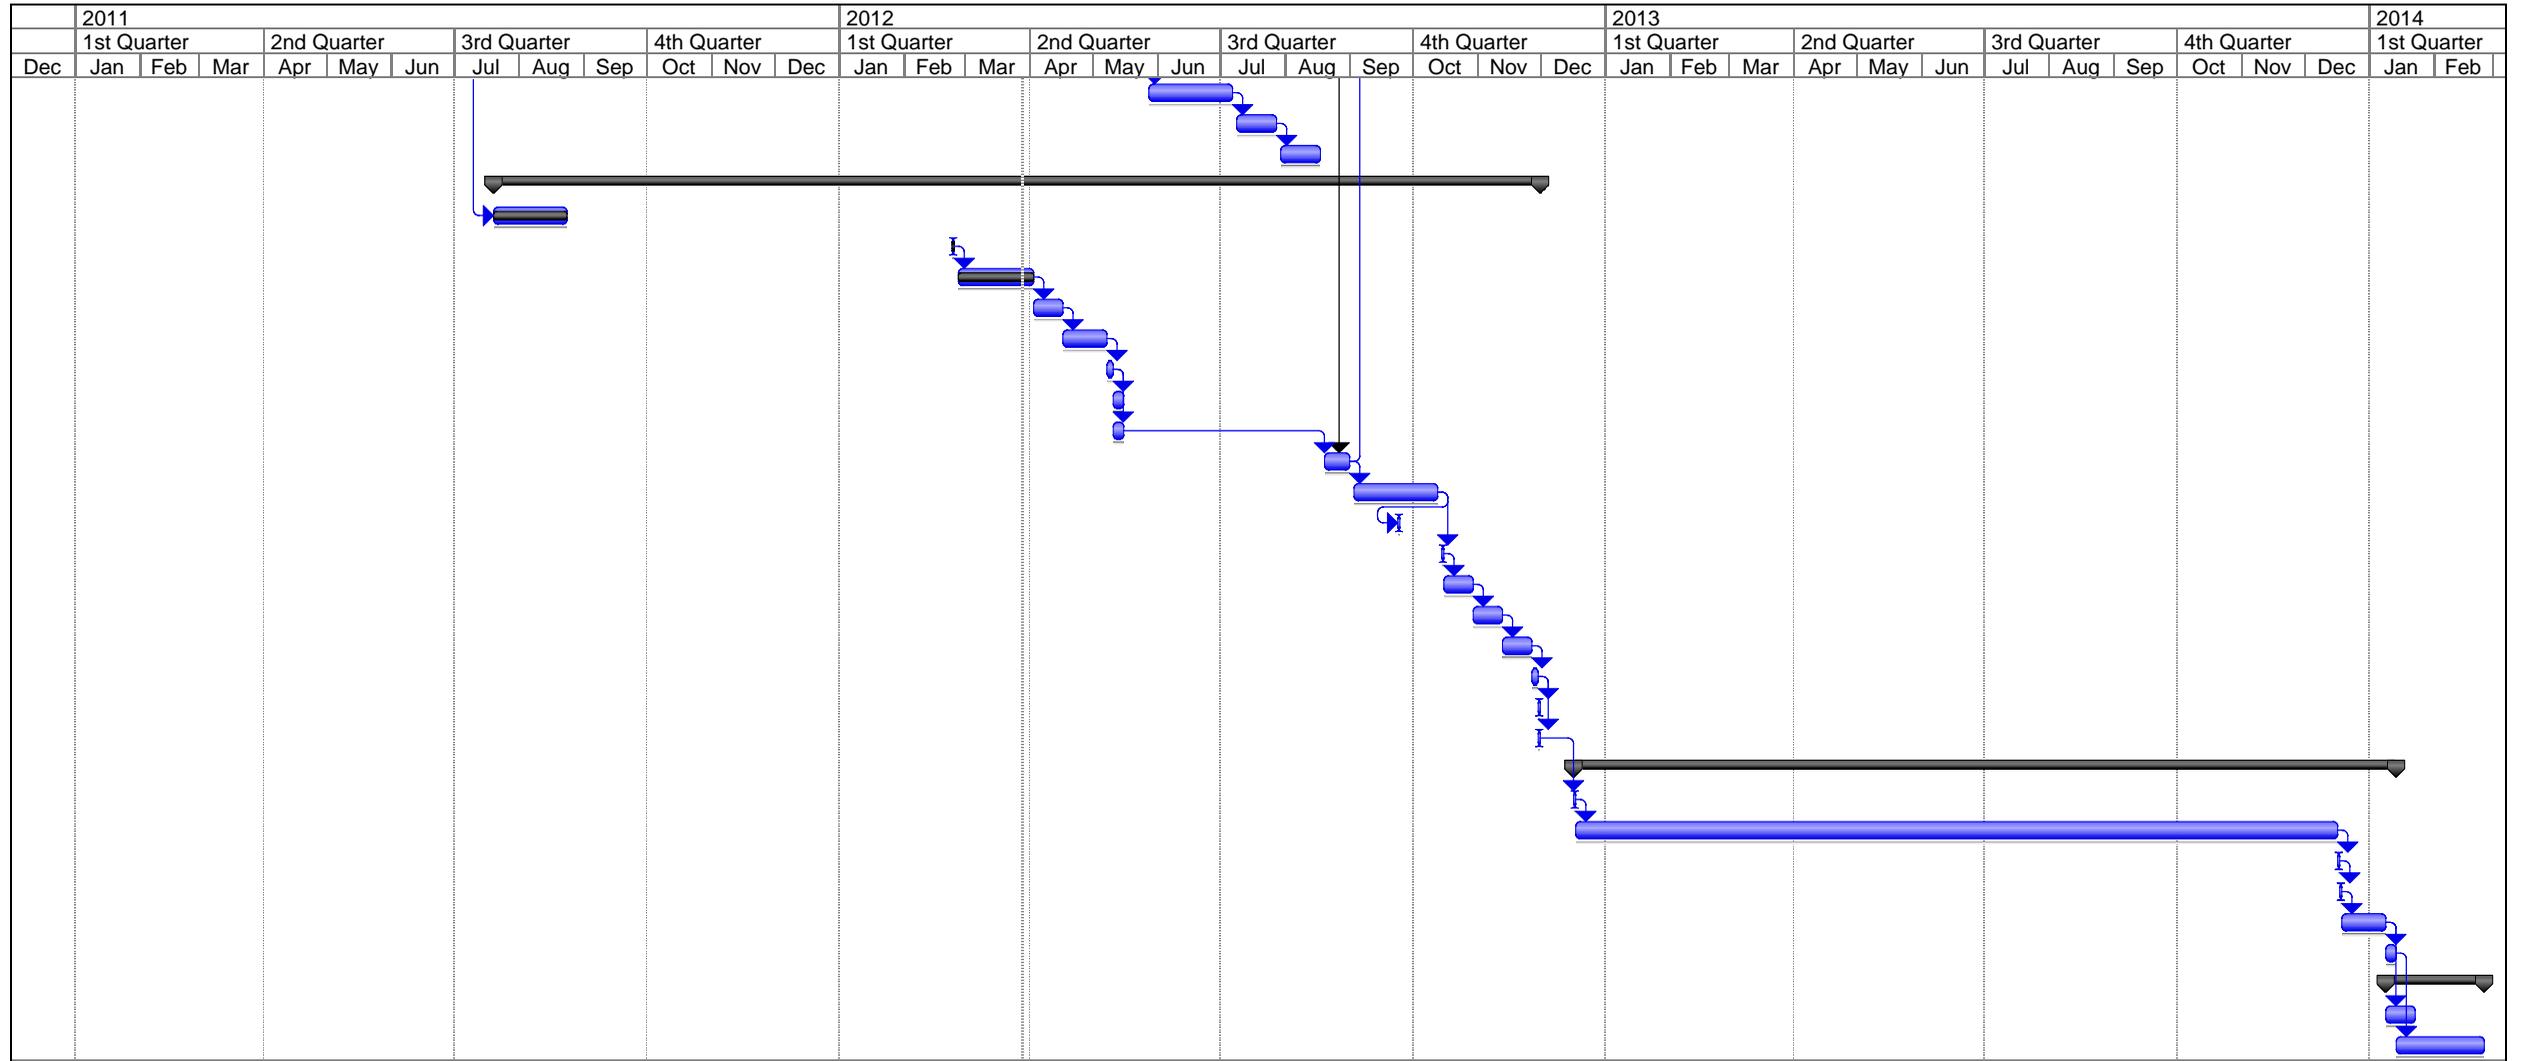

Project: AKV292 Seldovia Schedule v1  
 Date: Wed 3/28/12

Task  
 Split



Progress  
 Milestone



Summary  
 Project Summary



External Tasks  
 External Milestone



Deadline



|             |     |     |     |             |     |     |             |     |     |             |     | 2015 |             |     |     |             |     |     |             |     |     |             |     | 2016 |             |     |     |             |     |     |             |     |     |             |     | 2017 |             |     |  |  |  |
|-------------|-----|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|------|-------------|-----|--|--|--|
| 2nd Quarter |     |     |     | 3rd Quarter |     |     | 4th Quarter |     |     | 1st Quarter |     |      | 2nd Quarter |     |     | 3rd Quarter |     |     | 4th Quarter |     |     | 1st Quarter |     |      | 2nd Quarter |     |     | 3rd Quarter |     |     | 4th Quarter |     |     | 1st Quarter |     |      | 2nd Quarter |     |  |  |  |
| Mar         | Apr | May | Jun | Jul         | Aug | Sep | Oct         | Nov | Dec | Jan         | Feb | Mar  | Apr         | May | Jun | Jul         | Aug | Sep | Oct         | Nov | Dec | Jan         | Feb | Mar  | Apr         | May | Jun | Jul         | Aug | Sep | Oct         | Nov | Dec | Jan         | Feb | Mar  | Apr         | May |  |  |  |
|             |     |     |     |             |     |     |             |     |     |             |     |      |             |     |     |             |     |     |             |     |     |             |     |      |             |     |     |             |     |     |             |     |     |             |     |      |             |     |  |  |  |

Project: AKV292 Seldovia Schedule v1  
Date: Wed 3/28/12

|       |   |           |   |                 |   |                    |   |          |   |
|-------|---|-----------|---|-----------------|---|--------------------|---|----------|---|
| Task  |  | Progress  |  | Summary         |  | External Tasks     |  | Deadline |  |
| Split |  | Milestone |  | Project Summary |  | External Milestone |  |          |   |

|             |     |     |     |             |     |     |             |     |     |             |     | 2015 |             |     |     |             |     |     |             |     |     |             |     | 2016 |             |     |     |             |     |     |             |     |     |             |     | 2017 |             |     |  |  |  |
|-------------|-----|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|------|-------------|-----|--|--|--|
| 2nd Quarter |     |     |     | 3rd Quarter |     |     | 4th Quarter |     |     | 1st Quarter |     |      | 2nd Quarter |     |     | 3rd Quarter |     |     | 4th Quarter |     |     | 1st Quarter |     |      | 2nd Quarter |     |     | 3rd Quarter |     |     | 4th Quarter |     |     | 1st Quarter |     |      | 2nd Quarter |     |  |  |  |
| Mar         | Apr | May | Jun | Jul         | Aug | Sep | Oct         | Nov | Dec | Jan         | Feb | Mar  | Apr         | May | Jun | Jul         | Aug | Sep | Oct         | Nov | Dec | Jan         | Feb | Mar  | Apr         | May | Jun | Jul         | Aug | Sep | Oct         | Nov | Dec | Jan         | Feb | Mar  | Apr         | May |  |  |  |
|             |     |     |     |             |     |     |             |     |     |             |     |      |             |     |     |             |     |     |             |     |     |             |     |      |             |     |     |             |     |     |             |     |     |             |     |      |             |     |  |  |  |

Project: AKV292 Seldovia Schedule v1  
Date: Wed 3/28/12

|       |   |           |   |                 |   |                    |   |          |   |
|-------|---|-----------|---|-----------------|---|--------------------|---|----------|---|
| Task  |  | Progress  |  | Summary         |  | External Tasks     |  | Deadline |  |
| Split |  | Milestone |  | Project Summary |  | External Milestone |  |          |   |
