ID		Task Name	Duration	Start	Finish	Predecessors
1		**Bethel Small Boat Harbor**	**533 days**	**Thu 7/1/10**	**Mon 7/16/12**	
2	✓	Kickoff Meeting	1 day	Thu 7/1/10	Thu 7/1/10	
3		**Develop PMP**	**529.82 days**	**Fri 7/2/10**	**Thu 7/12/12**	
11	✓	Site Visit	1 day	Thu 9/9/10	Thu 9/9/10	
12	✓	Trip Report	11 days	Fri 9/10/10	Fri 9/24/10	11
13	✓	**Public Involvement**	**305 days**	**Wed 10/6/10**	**Tue 12/6/11**	**12**
15	✓	**Engineering and Design**	**403 days**	**Thu 7/1/10**	**Tue 1/17/12**	
26	✓	**Review (ITR)**	**6 days**	**Tue 1/10/12**	**Tue 1/17/12**	
30	✓	**Environmental (EA)**	**200 days**	**Tue 6/21/11**	**Mon 3/26/12**	
41	✓	**Real Estate**	**532 days**	**Fri 7/2/10**	**Mon 7/16/12**	
44	✓	**Cost Estimate**	**69 days**	**Thu 4/28/11**	**Tue 8/2/11**	
46	✓	**Project Complete**	**28 days**	**Mon 3/12/12**	**Wed 4/18/12**	
52		**Bethel O&M - Launch Ramps Construction**	**775 days**	**Wed 2/15/12**	**Tue 2/3/15**	
53	✓	Receive Denali Commission Funds	1 day	Tue 6/26/12	Tue 6/26/12	
54	✓	Signed MOA with Bethel	21 days	Fri 6/15/12	Fri 7/13/12	
55	✓	Recevie City of Bethel Funds	3 days	Mon 7/16/12	Wed 7/18/12	54
56	✓	Received O&M Funds	9 days	Wed 2/15/12	Mon 2/27/12	
57	✓	Revise Plans & Specs	1 day	Mon 4/23/12	Tue 6/12/12	
58	✓	Bid Schedule	6 days	Mon 5/28/12	Mon 6/4/12	57
59	✓	NEPA Amendment - Signed by COL	10 days	Tue 3/13/12	Mon 3/26/12	56FS+10 days
60	✓	Real Estate Certification from City	30 days	Mon 6/4/12	Fri 7/13/12	
61		**IFB**	**174 days**	**Wed 2/22/12**	**Mon 10/22/12**	
62	✓	Description of Scope	1 day	Wed 2/22/12	Wed 2/22/12	56
63	✓	Sources Sought	21 days	Fri 3/16/12	Fri 4/13/12	62
64	✓	2579	11 days	Tue 6/12/12	Tue 6/26/12	63
65	✓	Front End Specs	60 days	Thu 2/23/12	Wed 5/16/12	62
66	✓	Front End - CT	28 days	Thu 4/26/12	Mon 6/4/12	62FS+45 days
67	✓	Advertise	12 days	Tue 7/3/12	Wed 7/18/12	73,66
68	✓	BCOE Review	10 days	Thu 7/5/12	Wed 7/18/12	66
69	✓	BCOE Backcheck	3 days	Wed 7/25/12	Fri 7/27/12	
70	✓	BCOE Certification	4 days	Mon 7/30/12	Thu 8/2/12	68,69
71	✓	Prepare for Legal Review	1 day	Fri 8/3/12	Fri 8/3/12	70
72	✓	Legal Review	3 days	Mon 8/6/12	Wed 8/8/12	71
73	✓	Peer Review	3 days	Mon 8/6/12	Wed 8/8/12	71
74		Solicitation	23 days	Thu 8/9/12	Mon 9/10/12	67,72,73
75	✓	Pre-proposal Conference	1 day	Thu 8/23/12	Thu 8/23/12	74FS-15 days
76		IGE	10 days	Fri 8/3/12	Thu 8/16/12	70
77		Bid Opens	1 day	Mon 9/10/12	Mon 9/10/12	
78		Verify Bids	5 days	Tue 9/11/12	Mon 9/17/12	77
79		Prepare Award Package	10 days	Tue 9/18/12	Mon 10/1/12	78

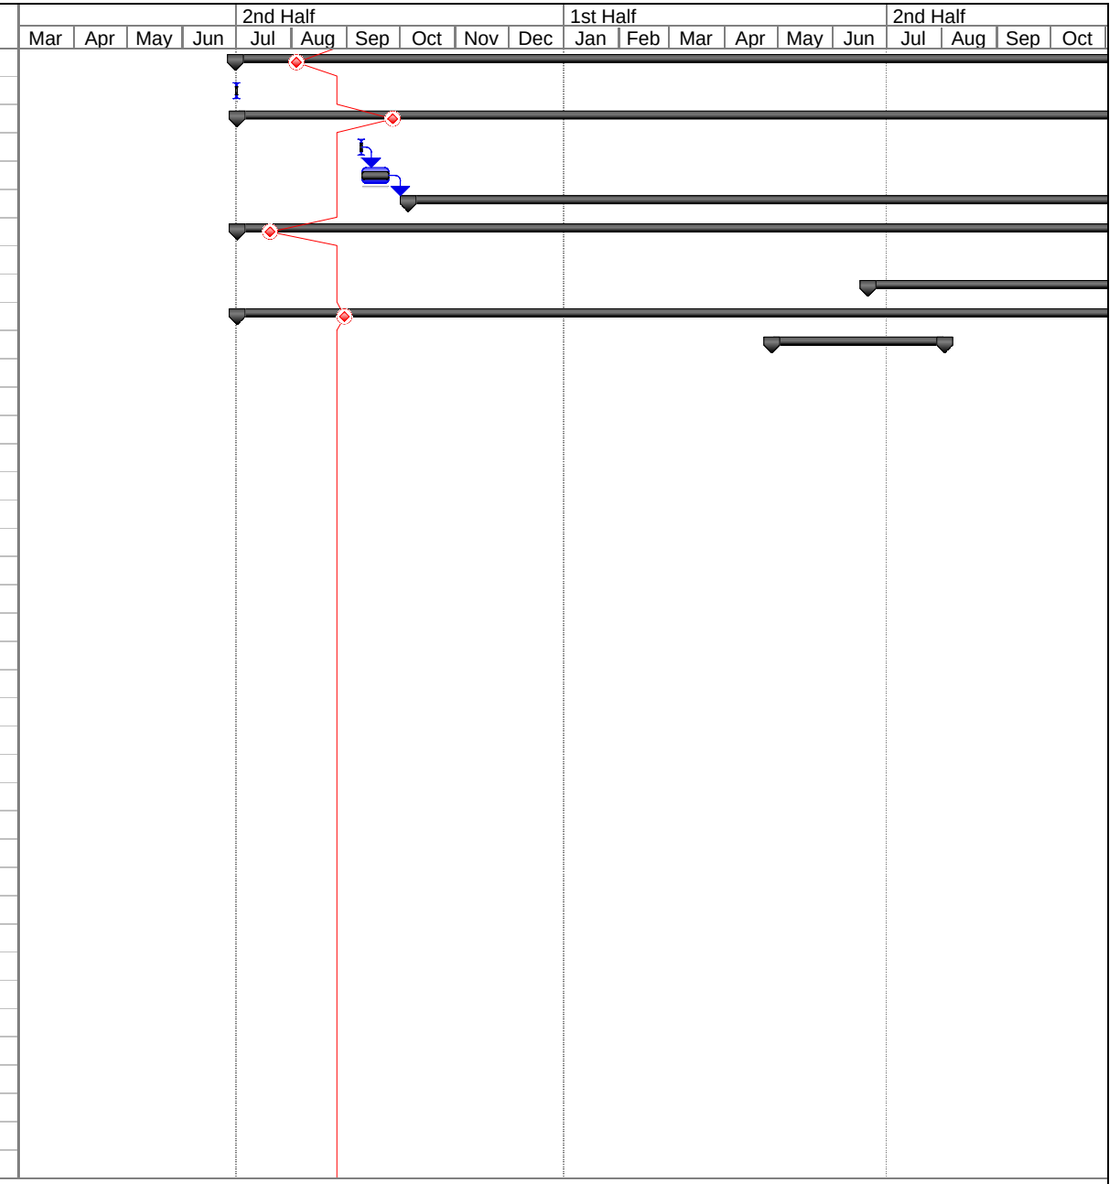

Project: Eek Draft Schedule 0.45mpp
Date: Thu 9/6/12

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

ID		Task Name	Duration	Start	Finish	Predecessors
80		Award	1 day	Tue 10/2/12	Tue 10/2/12	79
81		Bonds	10 days	Wed 10/3/12	Tue 10/16/12	80
82		Legal Review	3 days	Wed 10/17/12	Fri 10/19/12	81
83		NTP	1 day	Mon 10/22/12	Mon 10/22/12	82
84		**Construction Phase**	**561 days**	**Tue 10/23/12**	**Tue 12/16/14**	
85		Pre-Construction Meeting	1 day	Tue 10/23/12	Tue 10/23/12	83
86		Construction	530 days	Wed 10/24/12	Tue 11/4/14	85
87		Construction Complete	1 day	Wed 11/5/14	Wed 11/5/14	86
88		Inspection Report	14 days	Thu 11/6/14	Tue 11/25/14	87
89		Contract Closeout	14 days	Wed 11/26/14	Mon 12/15/14	88
90		After Action Review	1 day	Tue 12/16/14	Tue 12/16/14	89
91		**Project Closeout**	**36 days**	**Tue 12/16/14**	**Tue 2/3/15**	
92		Physical Closeout	3 days	Tue 12/16/14	Thu 12/18/14	89
93		Financial Closeout	30 days	Fri 12/19/14	Thu 1/29/15	92
94		Closed Out	3 days	Fri 1/30/15	Tue 2/3/15	93

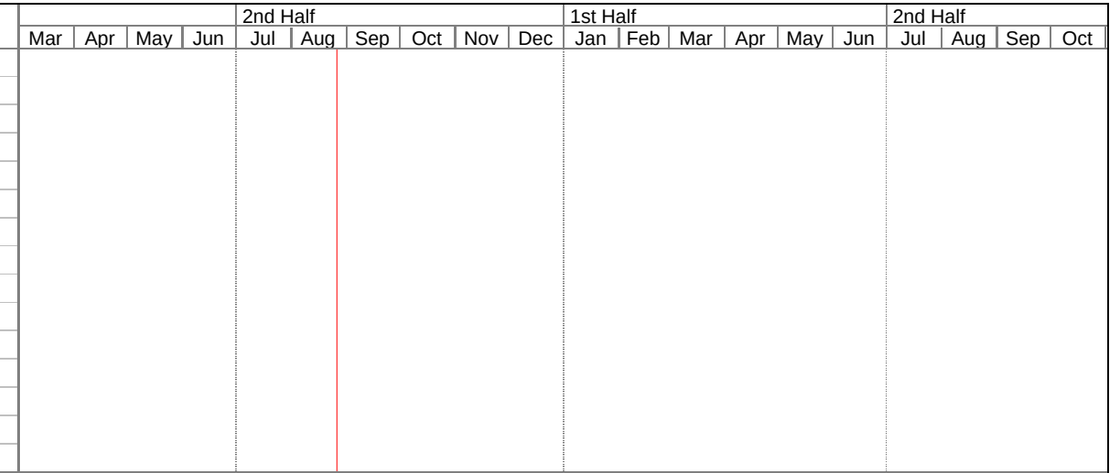

Project: Eek Draft Schedule 0.45mpp
Date: Thu 9/6/12

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

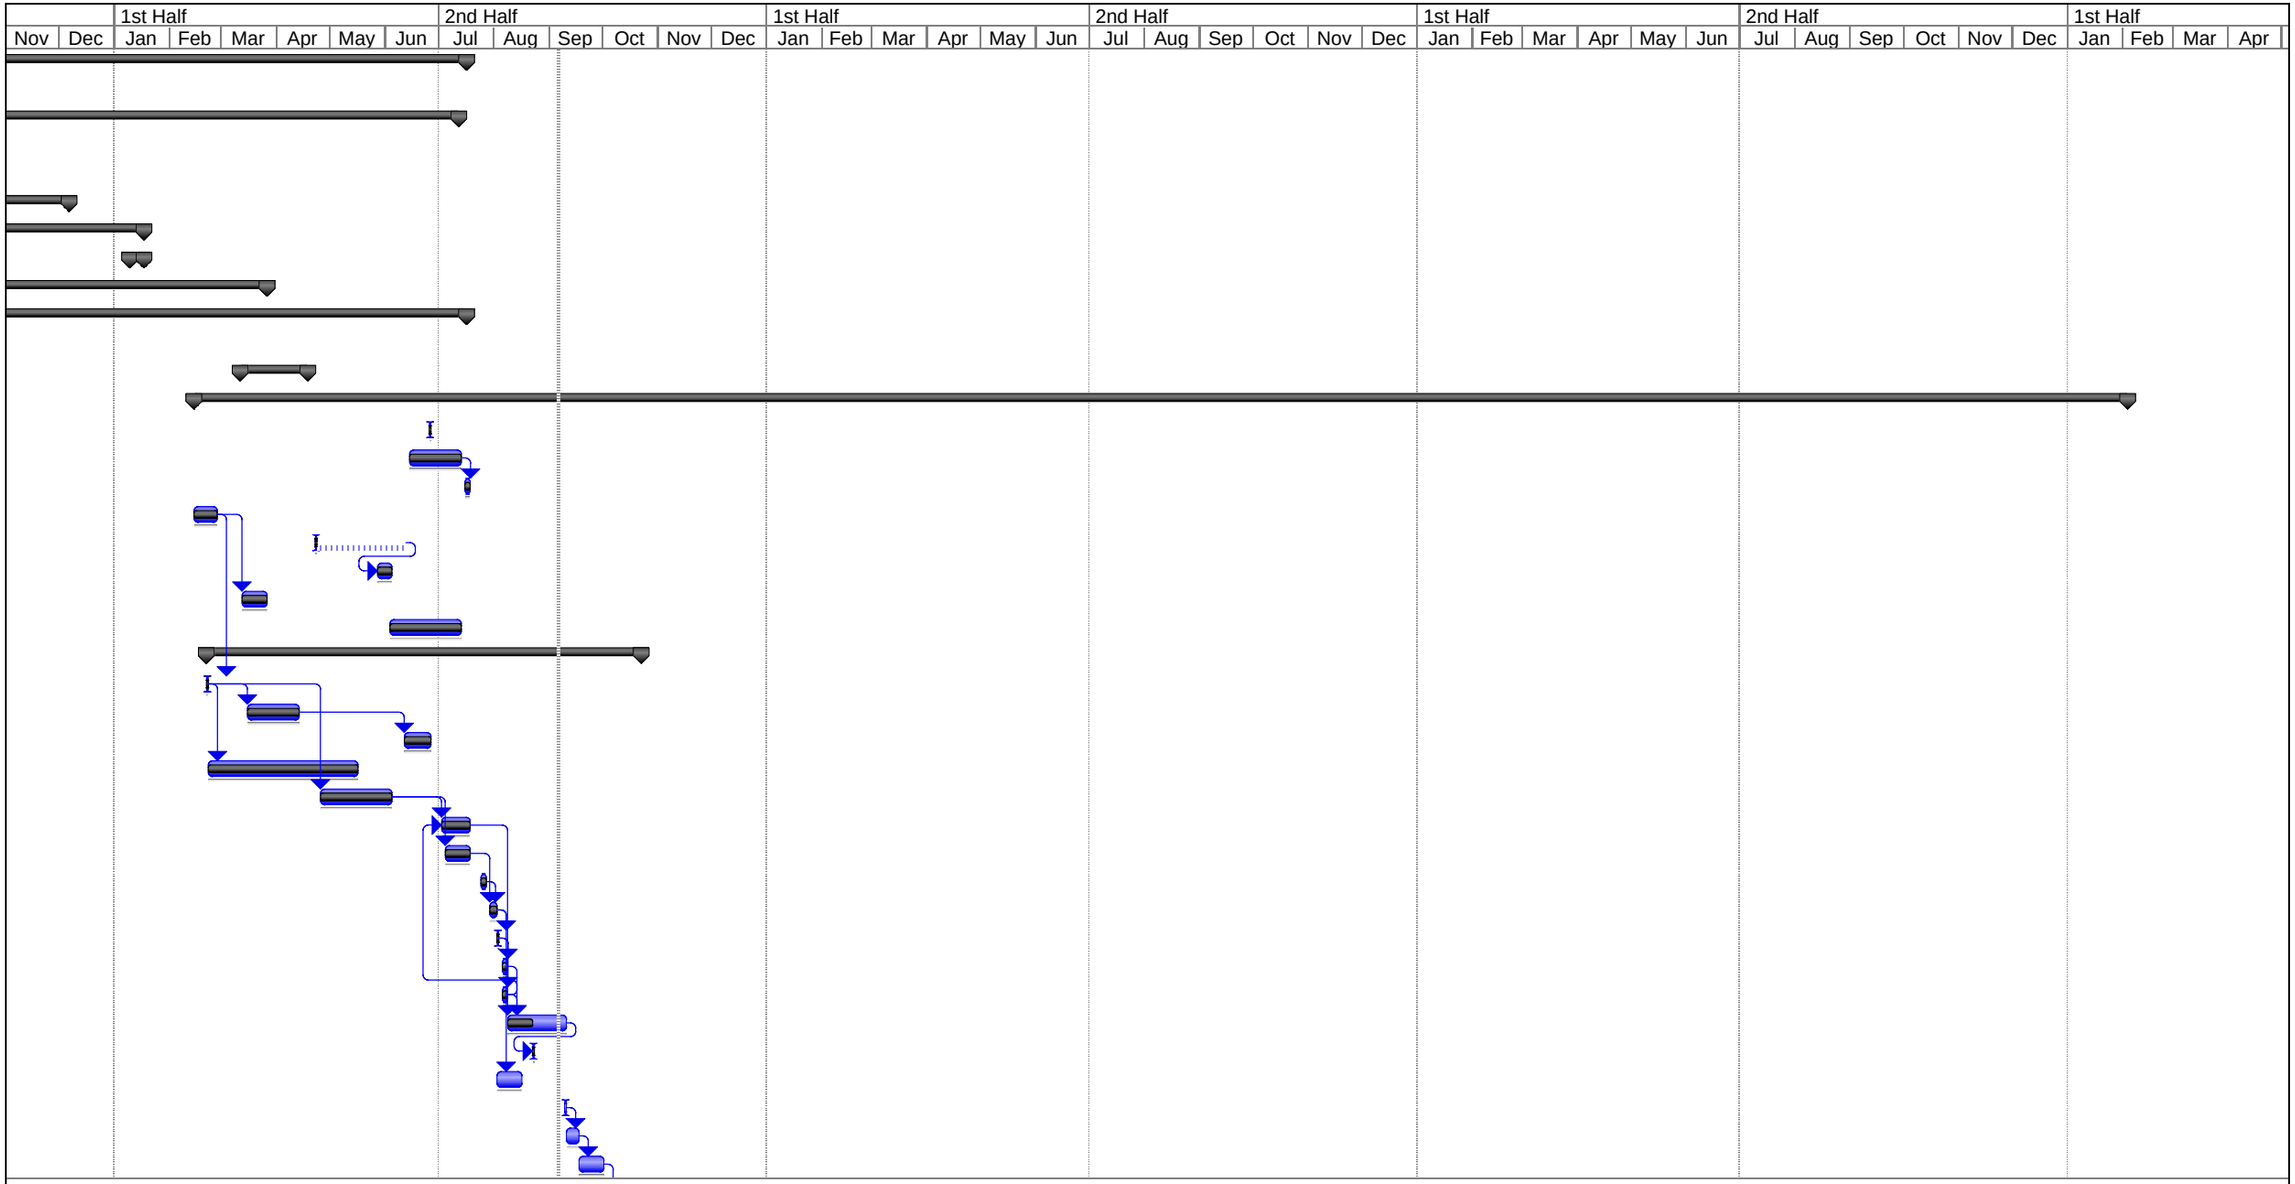

Project: Eek Draft Schedule 0.45mpp
Date: Thu 9/6/12

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

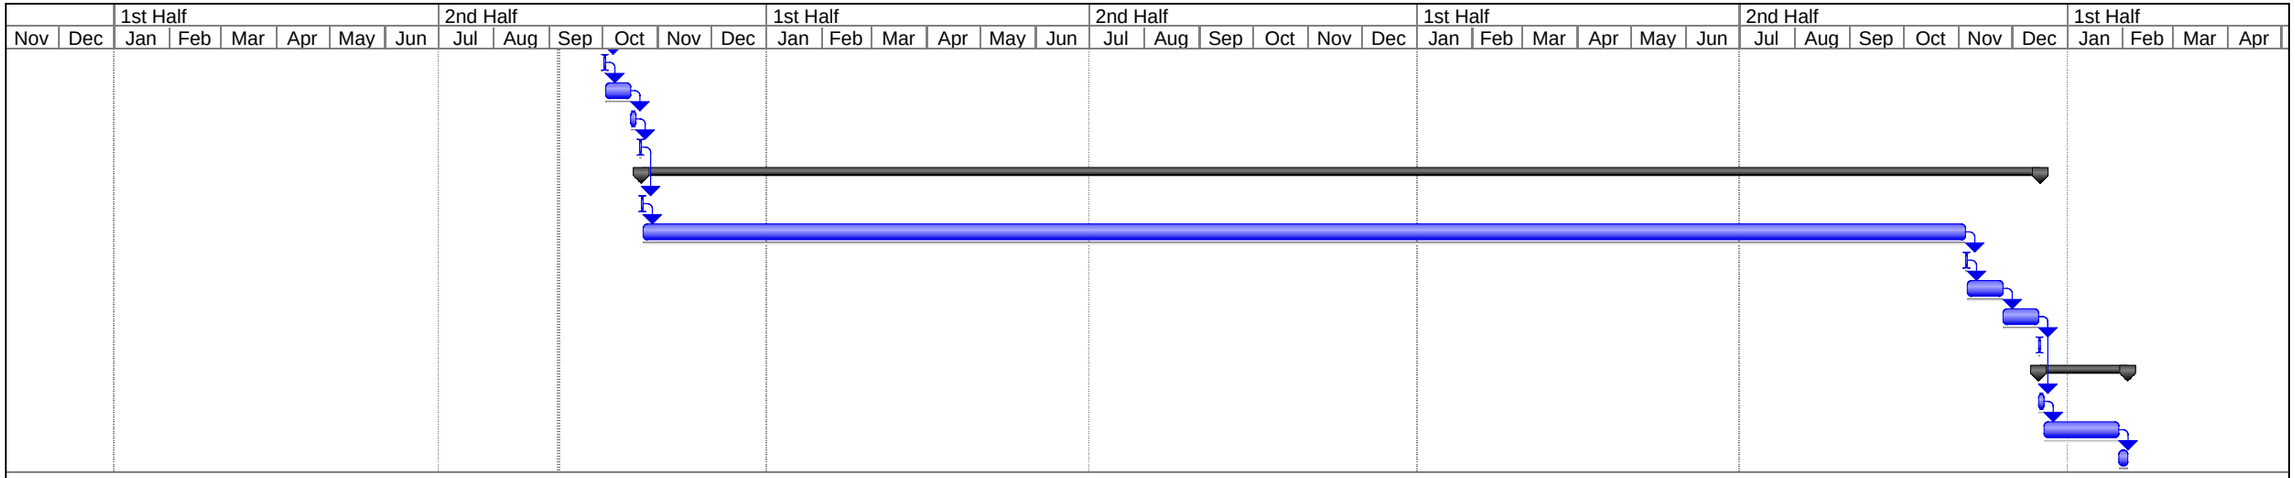

Project: Eek Draft Schedule 0.45mpp
Date: Thu 9/6/12

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
