ID		Task Name	Duration	Start	Finish	Predecessors
1		**Bethel Small Boat Harbor**	**533 days**	**Thu 7/1/10**	**Mon 7/16/12**	
2	✓	Kickoff Meeting	1 day	Thu 7/1/10	Thu 7/1/10	
3		**Develop PMP**	**529.82 days**	**Fri 7/2/10**	**Thu 7/12/12**	
11	✓	Site Visit	1 day	Thu 9/9/10	Thu 9/9/10	
12	✓	Trip Report	11 days	Fri 9/10/10	Fri 9/24/10	11
13	✓	**Public Involvement**	**305 days**	**Wed 10/6/10**	**Tue 12/6/11**	**12**
15	✓	**Engineering and Design**	**403 days**	**Thu 7/1/10**	**Tue 1/17/12**	
26	✓	**Review (ITR)**	**6 days**	**Tue 1/10/12**	**Tue 1/17/12**	
30	✓	**Environmental (EA)**	**200 days**	**Tue 6/21/11**	**Mon 3/26/12**	
41	✓	**Real Estate**	**532 days**	**Fri 7/2/10**	**Mon 7/16/12**	
44	✓	**Cost Estimate**	**69 days**	**Thu 4/28/11**	**Tue 8/2/11**	
46	✓	**Project Complete**	**28 days**	**Mon 3/12/12**	**Wed 4/18/12**	
52		**Bethel O&M - Launch Ramps Construction**	**538 days**	**Wed 2/15/12**	**Fri 3/7/14**	
53	✓	Receive Denali Commission Funds	1 day	Tue 6/26/12	Tue 6/26/12	
54	✓	Signed MOA with Bethel	21 days	Fri 6/15/12	Fri 7/13/12	
55	✓	Recevie City of Bethel Funds	3 days	Mon 7/16/12	Wed 7/18/12	54
56	✓	Received O&M Funds	9 days	Wed 2/15/12	Mon 2/27/12	
57	✓	Revise Plans & Specs	1 day	Mon 4/23/12	Tue 6/12/12	
58	✓	Bid Schedule	6 days	Mon 5/28/12	Mon 6/4/12	57
59	✓	NEPA Amendment - Signed by COL	10 days	Tue 3/13/12	Mon 3/26/12	56FS+10 days
60	✓	Real Estate Certification from City	30 days	Mon 6/4/12	Fri 7/13/12	
61	✓	**IFB**	**167 days**	**Wed 2/22/12**	**Thu 10/11/12**	
84		**Construction Phase**	**291 days**	**Fri 12/7/12**	**Fri 1/17/14**	
85	✓	Pre-Construction Meeting	1 day	Fri 12/7/12	Fri 12/7/12	
86		Construction	260 days	Mon 12/10/12	Fri 12/6/13	85
87		Construction Complete	1 day	Mon 12/9/13	Mon 12/9/13	86
88		Inspection Report	14 days	Tue 12/10/13	Fri 12/27/13	87
89		Contract Closeout	14 days	Mon 12/30/13	Thu 1/16/14	88
90		After Action Review	1 day	Fri 1/17/14	Fri 1/17/14	89
91		**Project Closeout**	**36 days**	**Fri 1/17/14**	**Fri 3/7/14**	
92		Physical Closeout	3 days	Fri 1/17/14	Tue 1/21/14	89
93		Financial Closeout	30 days	Wed 1/22/14	Tue 3/4/14	92
94		Closed Out	3 days	Wed 3/5/14	Fri 3/7/14	93

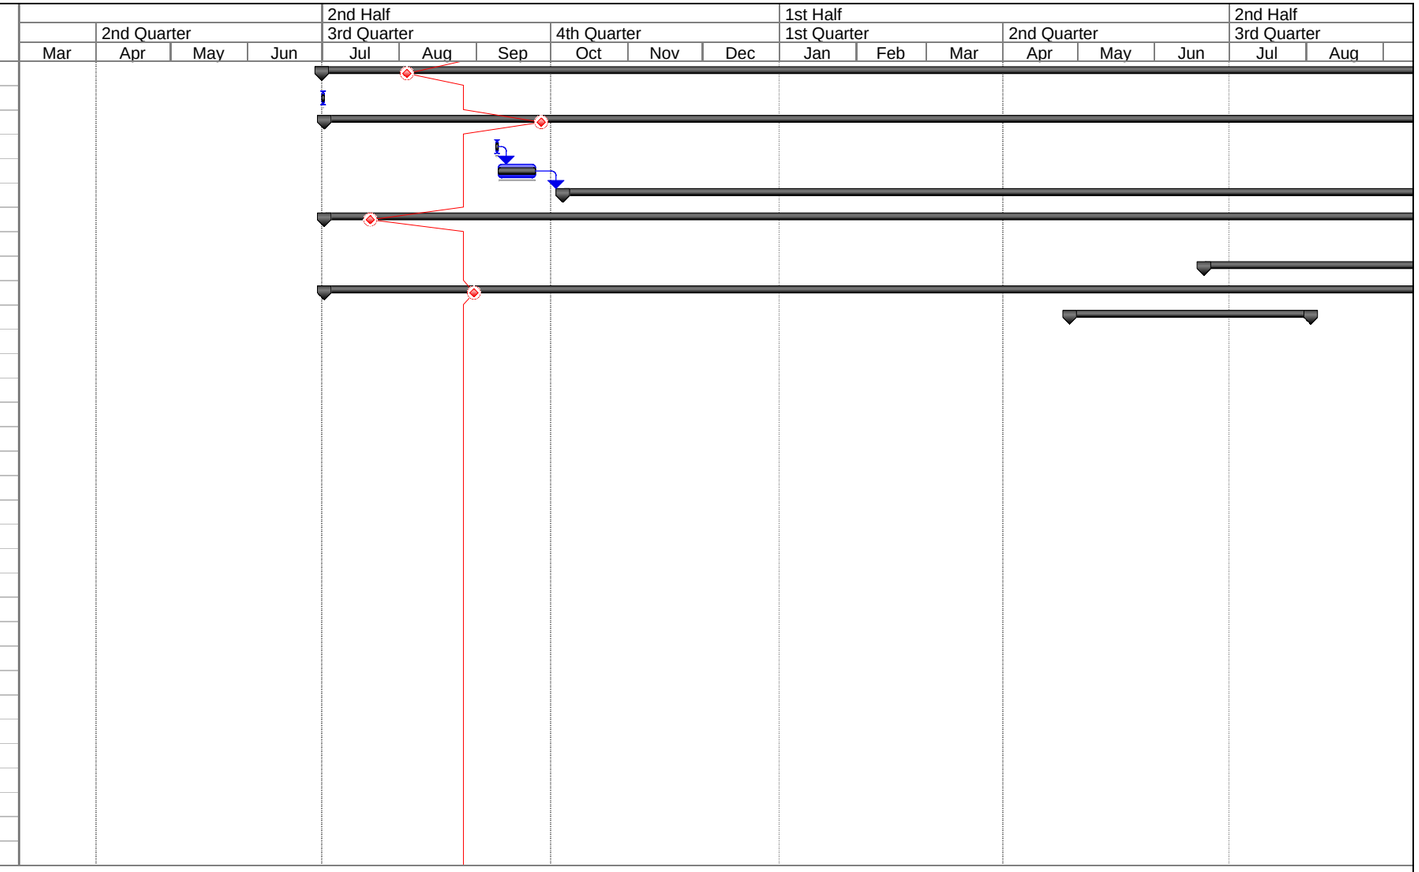

Project: Eek Draft Schedule 0.45mpp
Date: Wed 4/3/13

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

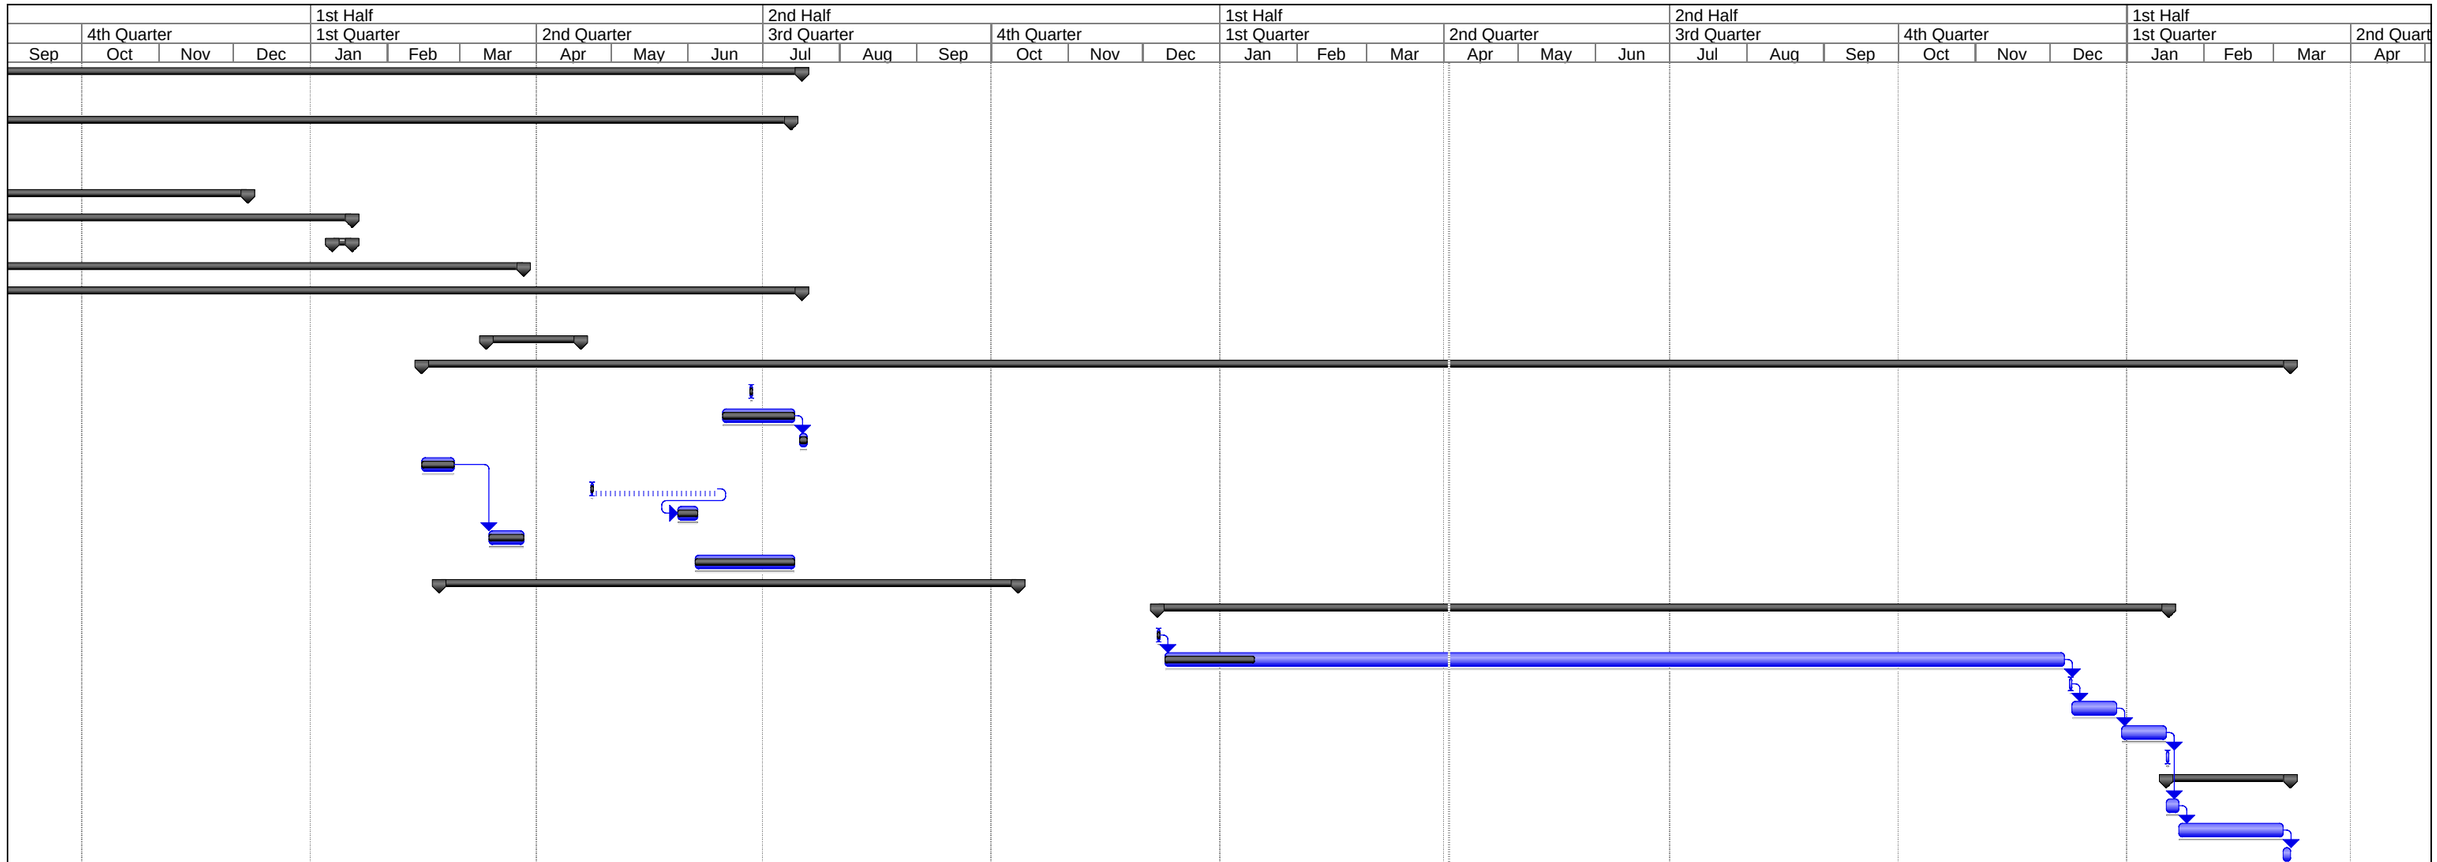

Project: Eek Draft Schedule 0.45mpp
Date: Wed 4/3/13

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
