Emmonak Landfill & Community Roads Project
Preliminary Schedule

ID	Task Name	Duration	Start	Finish
1	**Emmonak Landfill & Community Roads Project**	**528.5 days**	**Fri 3/1/13**	**Fri 9/12/14**
2	Submittals & Procurement	60 days	Fri 3/1/13	Fri 5/3/13
3	Mobilization	112 days	Fri 5/3/13	Fri 8/30/13
4	Procure and Barge Select A Material	30 days	Tue 7/9/13	Sat 8/10/13
5	Survey Culverts 2013	14 days	Sat 8/10/13	Sat 8/24/13
6	Survey OG if Required	4 days	Sat 9/7/13	Thu 9/12/13
7	Line work poles and guys 2013	14 days	Thu 9/12/13	Fri 9/27/13
8	Fall Shut Down	118 days	Thu 9/12/13	Wed 1/15/14
9	Haul and Place 2' Lift on Landfill Road	30 days	Wed 1/15/14	Sat 2/15/14
10	Haul and Stockpile Remaining Borrow	24 days	Sat 2/15/14	Thu 3/13/14
11	Select A to Culvert Crossing	10 days	Thu 3/13/14	Mon 3/24/14
12	Spring Shut Down	80 days	Mon 3/24/14	Tue 6/17/14
13	Survey 2014	5 days	Tue 6/17/14	Mon 6/23/14
14	Install 48" Culvert	10 days	Mon 6/23/14	Thu 7/3/14
15	Procure and Barge Surface Course	20 days	Mon 6/23/14	Mon 7/14/14
16	Haul and Place Borrow Delta Street and Emmonak Street	14 days	Fri 6/27/14	Sat 7/12/14
17	Haul and Place Borrow Delta and Third	7 days	Sat 7/12/14	Sat 7/19/14
18	Finish Borrow Community Roads	9 days	Sat 7/19/14	Tue 7/29/14
19	Surface Course community Roads	10 days	Tue 7/29/14	Fri 8/8/14
20	Dust Palliative community Roads	7 days	Sat 8/9/14	Sat 8/16/14
21	Community roads Culvert installation	21 days	Sat 7/5/14	Mon 7/28/14
22	Landfill Road Culverts	5 days	Mon 7/28/14	Fri 8/1/14
23	Haul Place Landfill Borrow above prior 2' Lift	14 days	Sat 8/2/14	Sat 8/16/14
24	Finish Landfill Borrow	4 days	Sat 8/16/14	Thu 8/21/14
25	Landfill road surface course	6 days	Thu 8/21/14	Wed 8/27/14
26	Dust Palliative Landfill Road	7 days	Wed 8/27/14	Thu 9/4/14
27	Signs	1 day	Thu 9/4/14	Fri 9/5/14
28	Project Cleanup and Demobilization	15 days	Wed 8/27/14	Fri 9/12/14

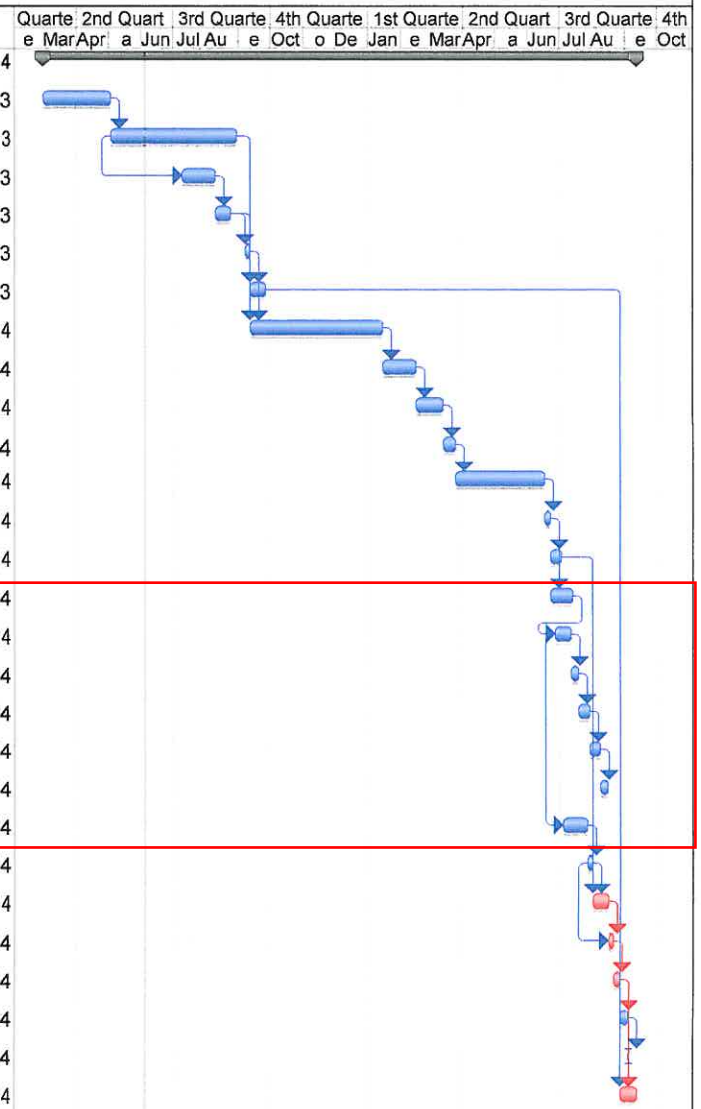

Project: Emmonak Community Roads Project Re
Date: Tue 6/4/13

Task		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Progress		Rolled Up Milestone	◇	Group By Summary	
Milestone	◆	Rolled Up Progress		Deadline	
Summary		Split			

Bering Pacific Construction
