


ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter
						Mar	Apr	May	Jun	Jul
1	<b>Bethel Small Boat Harbor</b>	<b>368.7 days</b>	<b>Thu 7/1/10</b>	<b>Tue 11/29/11</b>						
2	Kickoff Meeting	1 day	Thu 7/1/10	Thu 7/1/10						100%
3	<b>Develop PMP</b>	<b>160.97 days</b>	<b>Fri 7/2/10</b>	<b>Fri 2/11/11</b>						
4	Draft PMP	48 days	Fri 7/2/10	Tue 12/14/10	2					
5	Develop Schedule	32 days	Mon 10/18/10	Tue 1/11/11	4					
6	Develop Budget	14 days	Mon 10/18/10	Thu 12/23/10	4					
7	PDT Review PMP	1 day	Wed 12/1/10	Wed 1/12/11	5,6					
8	Customer Review of PMP	5 days	Thu 12/2/10	Wed 1/19/11	7					
9	Finalize PMP	13 days	Thu 12/9/10	Fri 2/4/11	8					
10	Approved PMP	5 days	Fri 2/4/11	Fri 2/11/11	9					
11	Site Visit	1 day	Thu 9/9/10	Thu 9/9/10						
12	Trip Report	11 days	Fri 9/10/10	Fri 9/24/10	11					
13	<b>Public Involvement</b>	<b>127.5 days</b>	<b>Wed 10/6/10</b>	<b>Fri 4/1/11</b>	<b>12</b>					
14	Community Resolutions	90 days	Wed 10/6/10	Fri 4/1/11	11					
15	<b>Engineering and Design</b>	<b>343.7 days</b>	<b>Thu 7/1/10</b>	<b>Wed 10/26/11</b>						
16	Surveys and Mapping	65 days	Thu 7/1/10	Tue 1/18/11	12					
17	Sampling	44 days	Wed 9/29/10	Mon 11/29/10	12					
18	Site Development	130 days	Mon 12/20/10	Fri 7/8/11	16,17					
19	Draft Design for PDT Review	30 days	Mon 6/20/11	Fri 8/19/11	18					
20	Incorporate Comments	3 days	Fri 8/19/11	Wed 8/24/11	19					
21	Section Chief Review	14 days	Wed 8/24/11	Tue 9/13/11	20					
22	Meeting with Customer on Design	1 day	Tue 9/13/11	Wed 9/14/11	21					
23	Final Design	30 days	Wed 9/14/11	Wed 10/26/11	22					
24	<b>Review (ITR)</b>	<b>24 days</b>	<b>Wed 10/26/11</b>	<b>Tue 11/29/11</b>						
25	Section Chiefs Review	14 days	Wed 10/26/11	Tue 11/15/11	23					
26	Incorporate Comments	5 days	Tue 11/15/11	Tue 11/22/11	25					
27	Backcheck	5 days	Tue 11/22/11	Tue 11/29/11	26					
28	<b>Environmental (EA)</b>	<b>171 days</b>	<b>Tue 1/18/11</b>	<b>Wed 9/14/11</b>						
29	SHPO	30 days	Tue 1/18/11	Tue 3/1/11	16					
30	F&W Coordination	30 days	Tue 1/18/11	Tue 3/1/11	16					
31	Section 404(b)(1) Analysis	30 days	Tue 1/18/11	Tue 3/1/11	16					
32	Record of Decision	30 days	Tue 1/18/11	Tue 3/1/11	16					
33	Section 103 Evaluation	30 days	Tue 1/18/11	Tue 3/1/11	16					
34	Statement of Findings	30 days	Tue 1/18/11	Tue 3/1/11	16					
35	CZM Consistency	60 days	Tue 1/18/11	Tue 4/12/11	16					


Project: Eek Draft Schedule 0.45mpp  
Date: Thu 12/2/10

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			


ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter	
						Mar	Apr	May	Jun	Jul	
36	Draft Final	80 days	Tue 1/18/11	Tue 5/10/11	16						
37	Pre-NEPA Meeting with Customer	1 day	Tue 5/10/11	Wed 5/11/11	36						
38	Public Review	30 days	Tue 7/26/11	Tue 9/6/11	44,37						
39	Sign FONSI	6 days	Tue 9/6/11	Wed 9/14/11	38						
40	<b>Real Estate</b>	<b>277.5 days</b>	<b>Fri 7/2/10</b>	<b>Tue 7/26/11</b>							
41	Ownership Identification	15 days	Fri 7/2/10	Thu 7/22/10	2						
42	<b>Obtain Permits for Construction?</b>	<b>135 days</b>	<b>Tue 1/18/11</b>	<b>Tue 7/26/11</b>							
43	From City	135 days	Tue 1/18/11	Tue 7/26/11	16						
44	State Tidelands	135 days	Tue 1/18/11	Tue 7/26/11	16						
45	<b>Cost Estimate</b>	<b>24 days</b>	<b>Wed 10/26/11</b>	<b>Tue 11/29/11</b>							
46	95% CWE	24 days	Wed 10/26/11	Tue 11/29/11	23						
47	<b>Project Complete</b>	<b>46 days</b>	<b>Fri 12/3/10</b>	<b>Fri 2/4/11</b>							
48	Publication/Reproduction	5 days	Fri 12/3/10	Thu 12/9/10							
49	Copies to Customer and Community	5 days	Fri 12/10/10	Thu 12/16/10	48						
50	Physical Closeout	3 days	Fri 12/17/10	Tue 12/21/10	49						
51	Transfer of Remaining Funds	30 days	Wed 12/22/10	Tue 2/1/11	50						
52	Fiscal Closeout	3 days	Wed 2/2/11	Fri 2/4/11	51						



Project: Eek Draft Schedule 0.45mpp Date: Thu 12/2/10	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

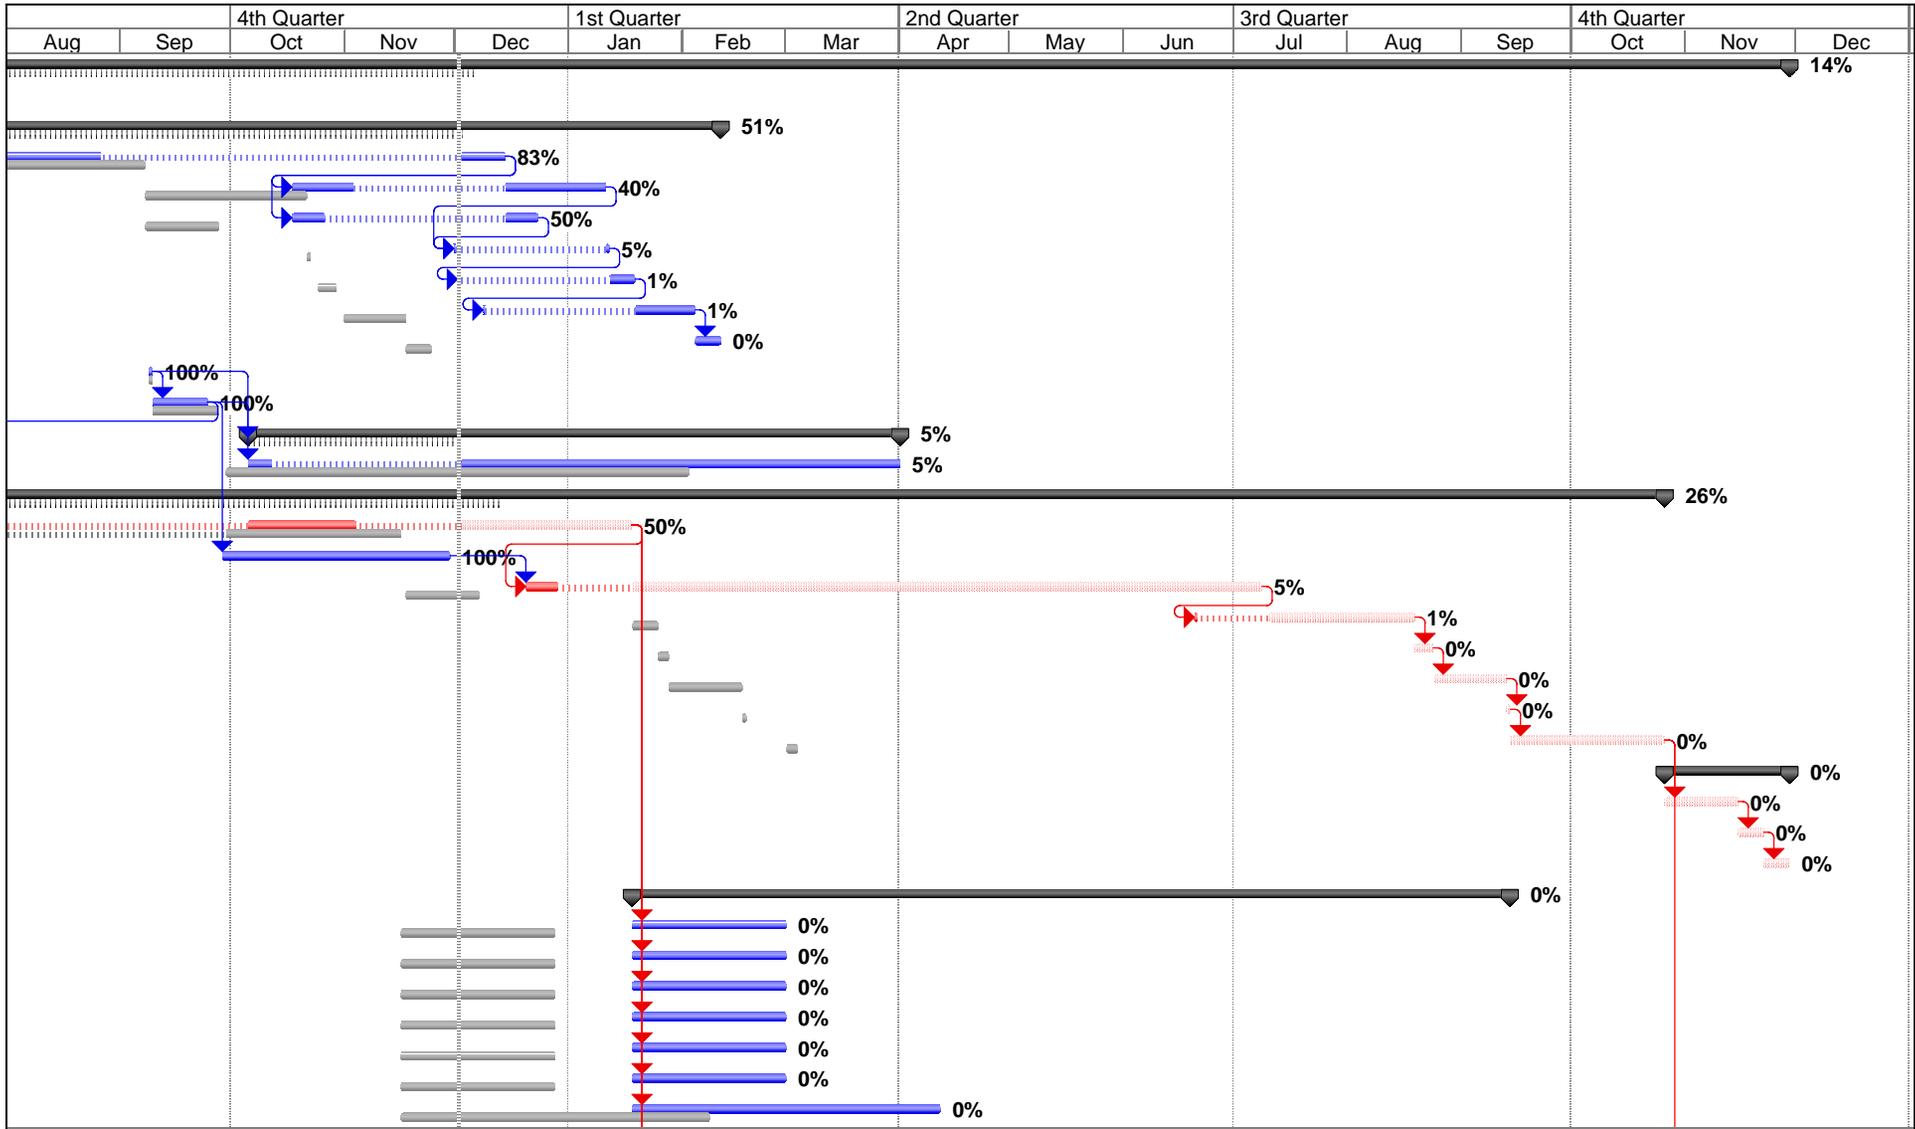

Project: Eek Draft Schedule 0.45mpp Date: Thu 12/2/10	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

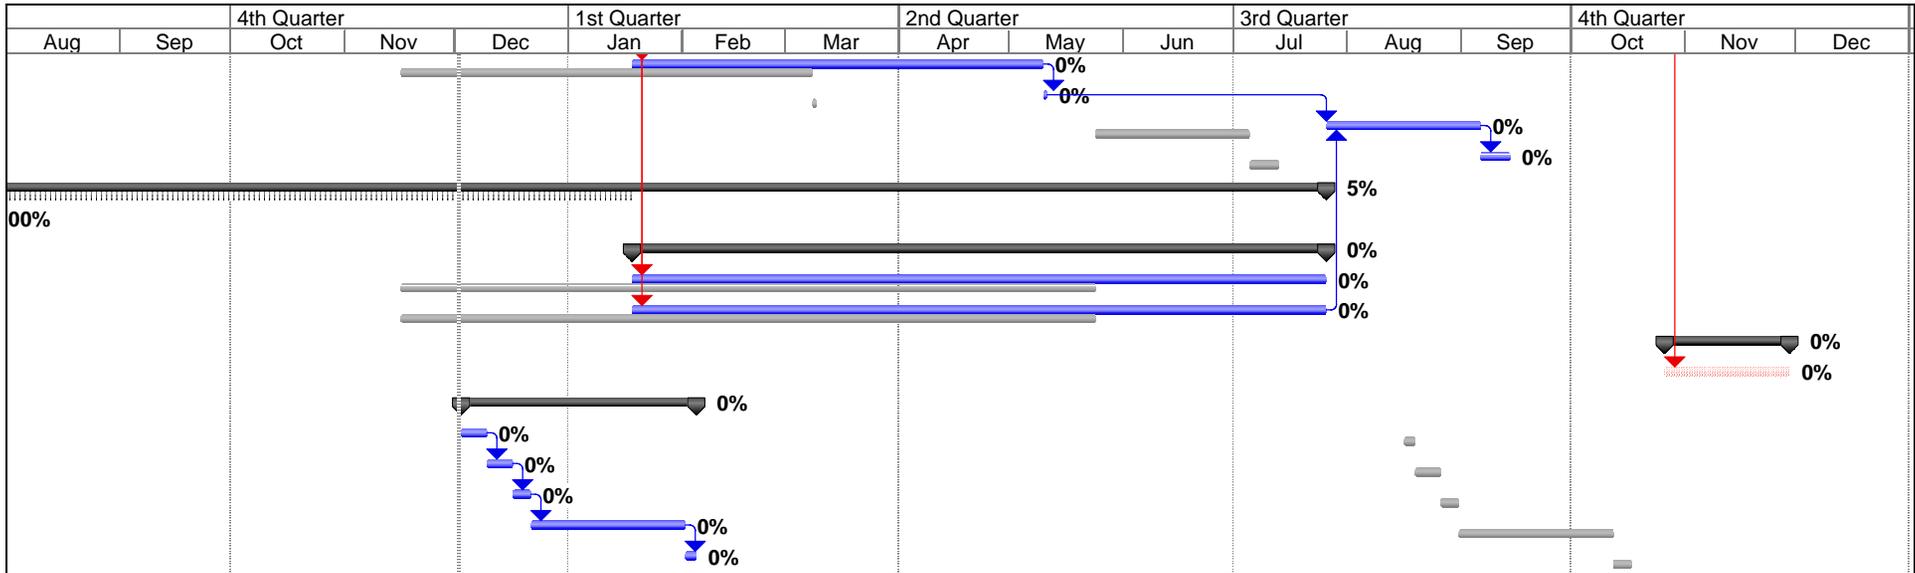

Project: Eek Draft Schedule 0.45mpp  
 Date: Thu 12/2/10

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			
